

R — G — P — F

Details of Buildings.

circa 1910 17" x 24"

A list giving map numbers,  
building numbers, date built,  
construction, dimensions  
(usually on ~~the~~ plan and  
elevation drawings), cubic  
contents and cost.

Gun Carriages

Mr P Faulkner  
 Sen Arch: Aest

DOE

Anc Mon 2<sup>d</sup>

Fortress House

---

referred to by

Mr A Colin Carpenter  
 DOE

Anc Mon 2<sup>d</sup>

1-3 Albert Road

Devonport  
Plymouth

Carriages made at Totnes

DRAWINGS SENT TO PSA

Building/Structure	New Bld No	Old Bld No	Drawing Ref(s)
Grand Magazine		1/3	C133
		1/6	C125
		1/7	C129
		1/8	C126
			5/1 C115 6/5 C213
Gunpowder Press House 1 & 2	L102)	103)	C244
	L103)	104)	L102.B.01
	L102)	103)	C244
	L103)	104)	L102.B.02
Gunpowder Mills Group C & D	L153	160 & 167	C150 W No 2
	L153/1	"	C149 W No 1
	L153/2	"	C149 W No 5
	L157/3	167	C87 X No 2
	L157/4	167	C88 X No 1
Group C & D (39 & 40)	L148/11	156	C230 L148.B.18
Gunpowder Mills Group G & F	L148	156	C230 X369
	L148/3	156	C232 X371
	L148/4	156	C231
	L145	152	C170
	L145/1	152	C172
Gunpowder Mills Group E (38)	L149	154	C113 L149.B.15
	L149/1	154	L149.B.05 C153
	L149/2	154	C153 L149.B.02
	L149/9	154	C130 L149.B.09
Walton House Offices	A200/1	219	C28 A200.B.05
	A200/3	219	C225 C83
	A200/4	219	219/1 A200.B.04
No 9 Powdermill Lane Offices	A269	264	A269.B.07 151/41

Building/Structure

Drawing Ref(s)

Lock and portion of canal

D53

Footbridge

51

Covered Boat

M343A  
B-01



# Anc Mon Insp, Requirements

No reqd	Maps	Reference
2	N Site (ca 1:2500) 1917	P17
2	S Site — " — — " —	P18
2	Motorway maps (DOT)	

## Drawings

2	Press House Complex (Lined)	C244
3	Powder boat drawing (Lined)	
2	Main laboratory (old No 144)	
2	Grand Maggijne	C133
	Lock	D53

## Cumford Mills

2	9 Poplars Mill Lane
2	Walton House
	Building Plan Book
2	All Bldgs looked at.

## Photographs

2	SM 1895 No 9 Press House 10x8	DONE.
	Record Photographs of Main Lab.	

REF.		PAGE
1	Grand Mag	1
103-44	Press House Complex	10
144.	Main Lab 144	15.
	GP Mills	17
	GP Mills	"
	→	"
	→	"
	→	"
	Walton House	24
	A 201/202	25
	9 Powdermill Lane	30?

BLDNG. No

PAGE

L 102

10

L 103

10

L 105

11

L 106

11

L 109

12

L 110

12

L 111

12

L 130

112

113

114

133

13

L 135/6/7/8/40 }

14

L 116, L126

LF 139 LF 156 HF 9

L 121 L144 L141 L122

15

L 127 LF 147

16

L149

L145

L148

L153

L157  
L149

17

L129

L154

L184

18

L161

L160/1/2

19

L167

H6/4/5/7/8

20

L 169/40/42

L 168

21

L164 L174	22
LE 176 (4/8/9/80	23
L183 A211 H10 A200	24
A201/2 AS 203/5	25
AS 221 H12 AF208 AS209	26
A 230/1/2	27
A 234/8/68 AB 243	28
AB 252/3/4/5/60/1/2/5 } A 253 H21	29
A 269	30
AS 280/1 A277/8/9 H 26	31
H 28/9 HS 30	32
HS 31/2 AE 275	33
HB 38 H 37	34
M 301	40
M 311/2/3	42
M 323 G-404 G-427 } G-E 403/5/6/7	45
GE 408/9 G-411/3	46
G-417 G-423	47
G-418 G-422	48
G-431 GE 440	49
G-441 G-443	50
G-435/4 G-452/4 N524 N518	51
G-415 G-421/6/9 N500	52
M 324/5 M 336/7 N503 N509 G-414	53
M 339 M 342/5	54



M346 N545	55
N 541/3 N550/1/2	56
N 544/8/9	57
M348 N553/4 P409 R652	58
M350/1/2	59
M319/70/349 N549	60
N <del>559</del> 567/9/41/3/4/6	61
N 556/7/62/3/6/8/42	62
N 564 NE565	63
R601/2/3/4/5/6/8/9/10/11/2/3 PF413	64
R614/5-20/22-25/27/28/31-35 R644-46/48-51/54/55 P412	65
P414/6 RF563 RS639	66
L101 L131/2	78
<del>L119</del> 114/9 L134/4 L143	79
L120/3/8 L146/4 L151/5	80
H3 L152/9	81
AE23/4 LF141	82
AE210 HE13	83
AB244/5/51 A235/6 H16	84
H17/8/9 HF20	85
A249 H23/5 HC24	86
H34 HB33 HF24 HS35	87
A227 AB251 L117 L131	88
GE400 MF317	89
G412/6/23 GE400/6	90

G 418	G 438	G 444		91
G 449	G 452/3	N 521		92
G 421	G 430	G S 436/9	N 518	93
N 505/6/8/9	N 3514	M 334)		94
	N 3511			
M 330	M 341/4			95
P 407/8				96
R 411	R 656 - 660/3/5-7			97
	R 641/2/3/6	R 629/42		
	R 638			
P 402	R 662	R 674	R 675	98
P 403/4/5/6	P 415			99
M 340	P 417/8/9/20/1/3/4			100
	P 422			

WASC 1509

SHEETS  
1 TO 10.  
BUILDINGS  
1 TO 104.

# Royal Gunpowder Factory



Nitro Glycerine Factory

Edmondsey Meud



*Handwritten note:* Royal Gunpowder

*Handwritten note:* C.O.P.

B



SHEETS  
11 to 30

BUILDINGS  
105 to 272

RIVER LEA

HEAD STRAITS

OLD RIVER

CONDITE

Queen Mead

Condite Factory

Little Hoppit

Great Hoppit

Gas Works

B.W. Dept.

Great Hoppit

Manager's Quarters

C

RIVER LEA NAVIGATION

Asphalt Store No. 1

Great Hoppit

Hospital

Acetone Factory

B.W. Dept.

Boat Ho.

Extruding Ho.

Am. Picnic House

Saltpetre Refinery

D.B. Office

HIGH BRIDGE STREET

Superintendents Quarters

Manager's Quarters

Mass. Club

Police Station

Library Billiard Rm.

A.S.W. Quarters

Manager's Quarters

Cashiers Qrs.

St Lawrence & Holy Cross Church

Lock

Old River Lea

Unltd. Wharf

Branstone Refinery

Lower Island

F.D. Room

Shifting Room

Kitchen

Scale Store

Scale Store

Fire Engine Ho.  
Water Works Ho.  
Dining Room

Tumbling Bay


No. 1 Incorporating Mill  
Car House No. 2

Lower Island

Granulating Ho.  
No. 2

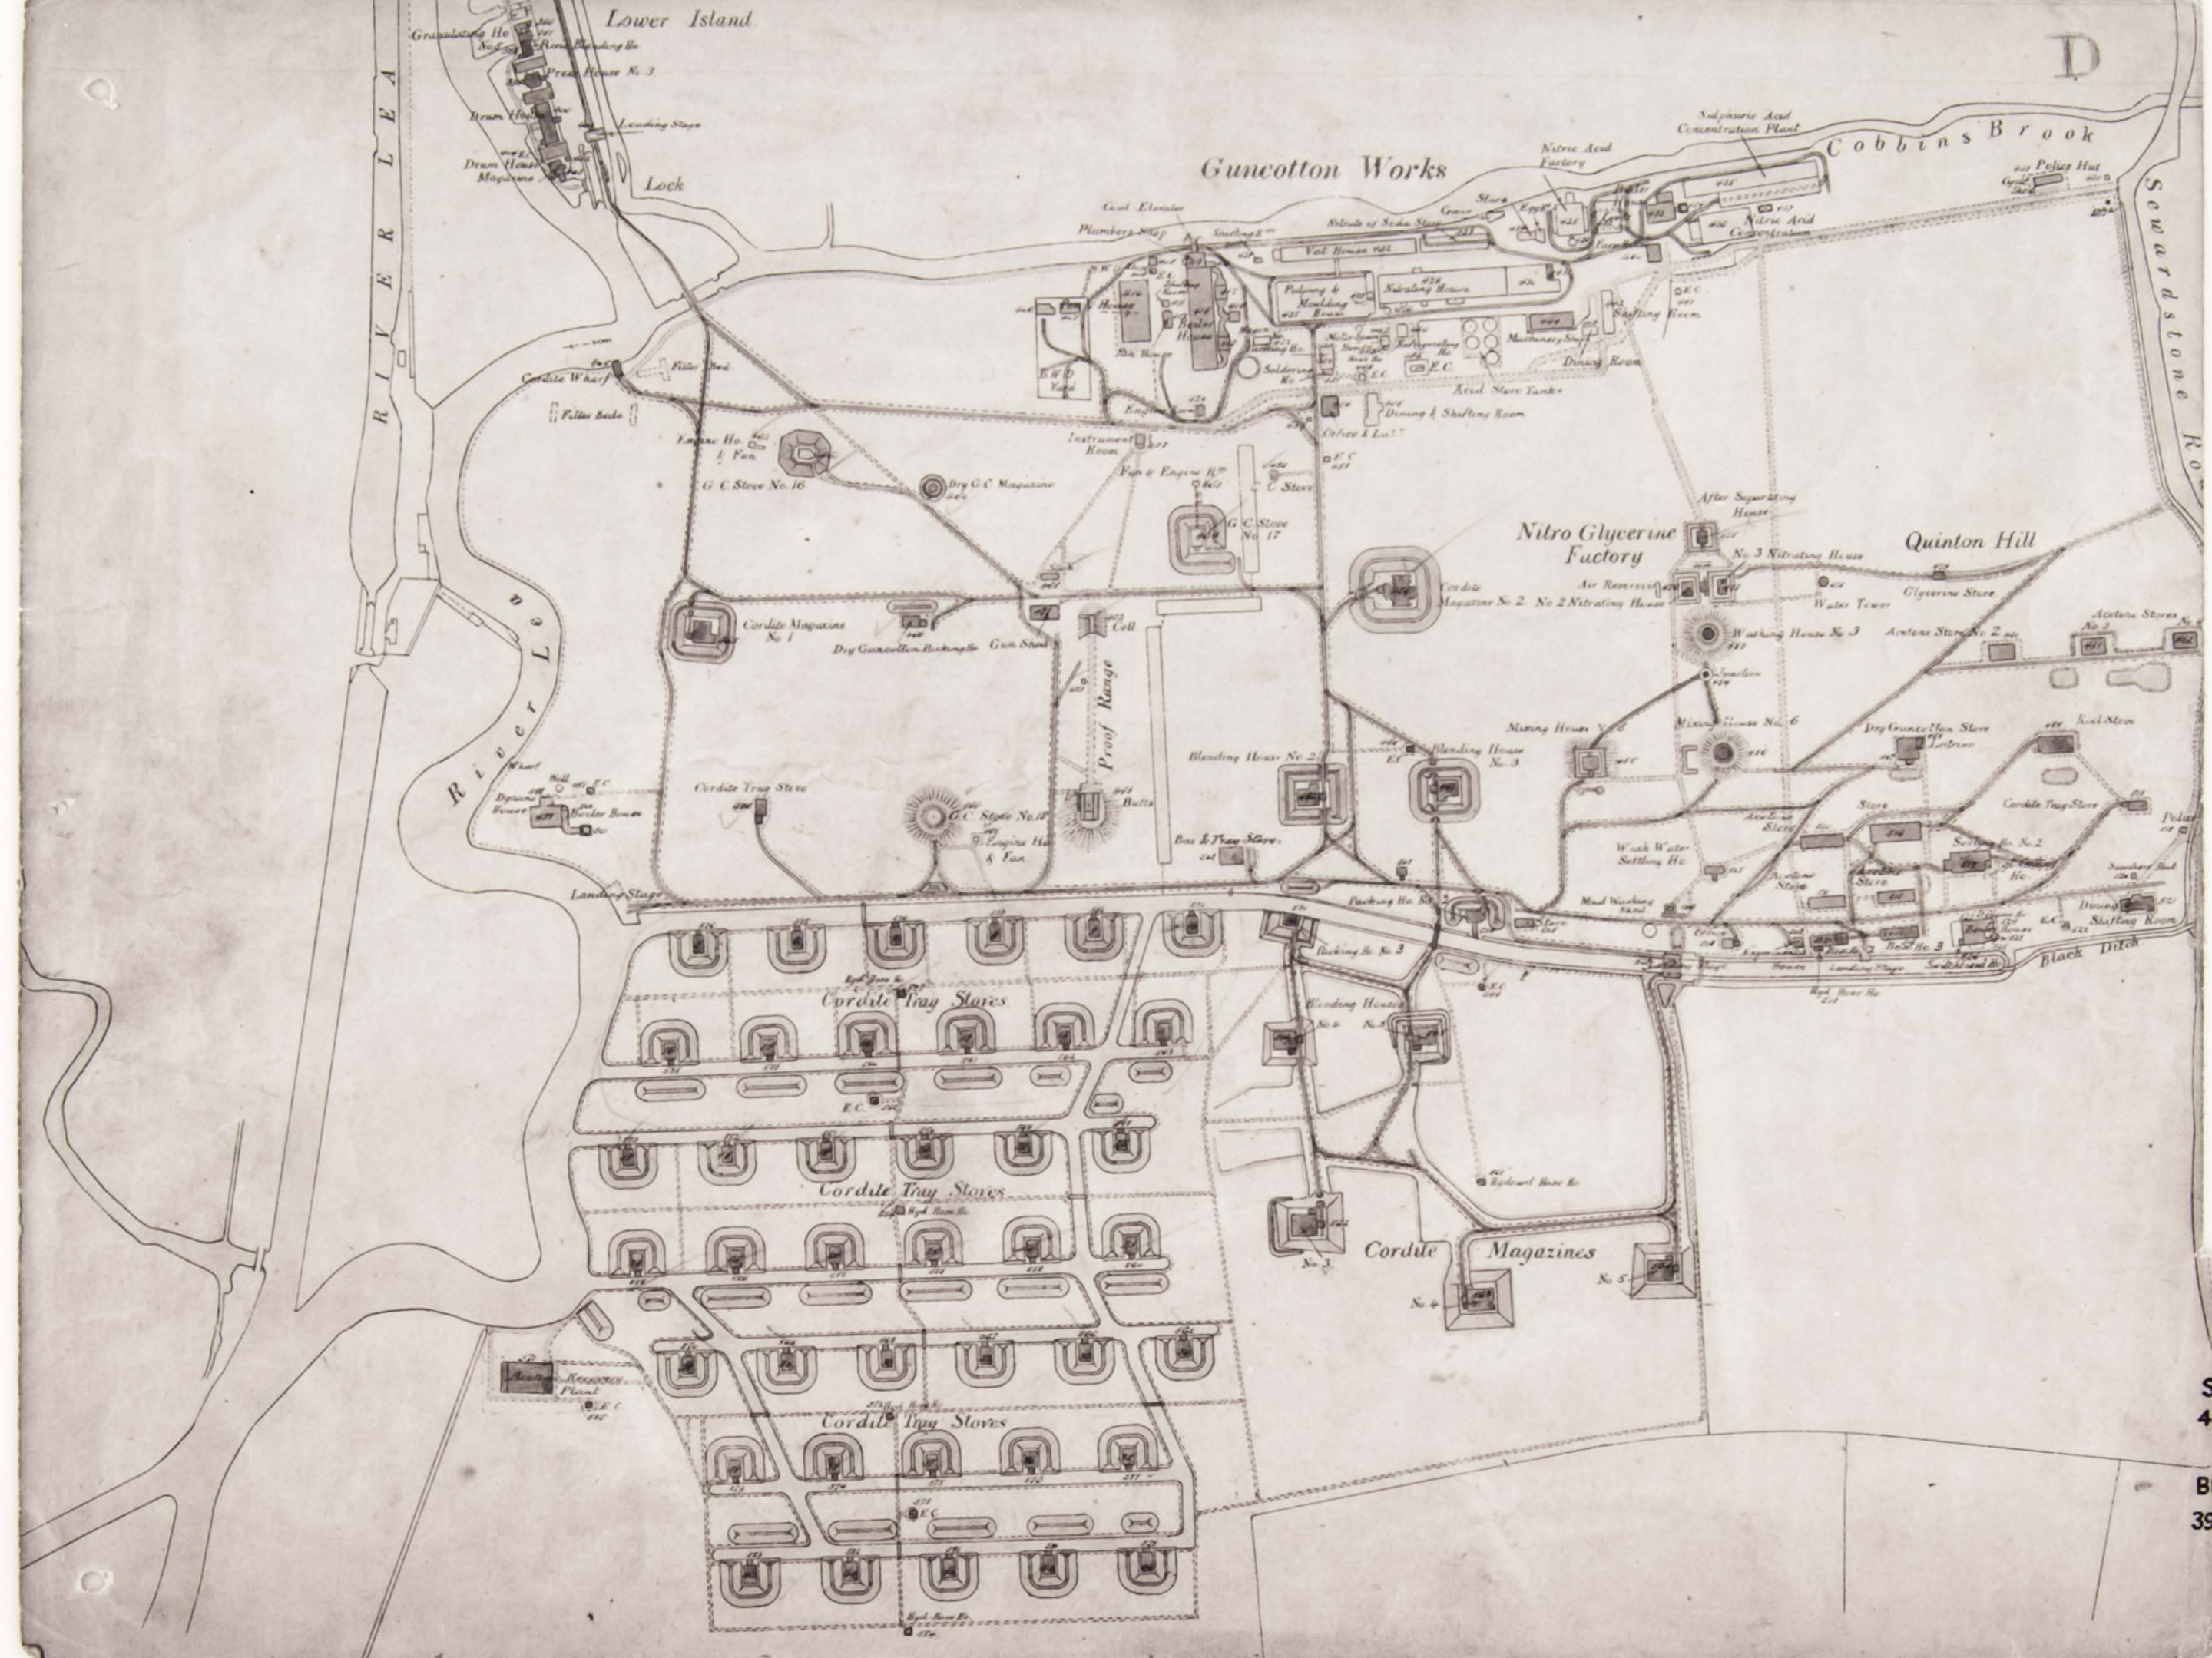
Car House No. 3

RIVER LEA NAVIGATION



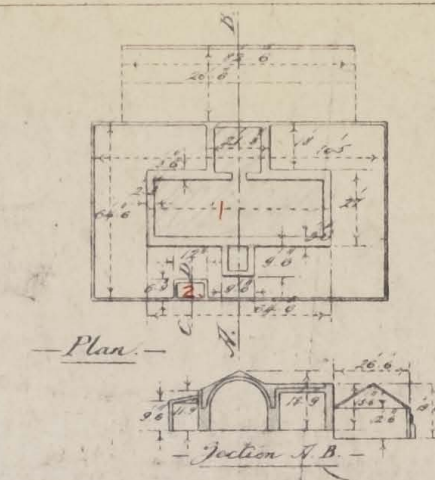


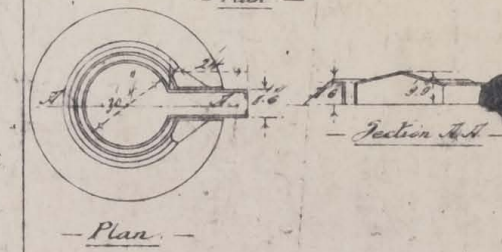



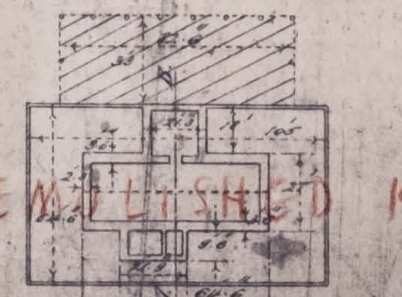

SHEETS  
31 to 42.

BUILDINGS  
273 to 395.











SHEETS  
43 TO 65.














BUILDINGS  
396 TO 585.

Map No.	Description	When built	Construction	Dimensions	Cubic Contents	Cost of Buildings where known	Price per Cubic foot		Depreciation	Valuation	Remarks	No.
							£	s. d.				
1	Wet Connection Magazine Barge Cover	1867-8	Brick, matchlined throughout Roof, brick and concrete, slate. Floor, Asphaltic or concrete. Brick. Roof, slates.		36804.0	£ 1840	1	0	✓		Not in Use	
2	Porch	-	Brick matchlined Roof concrete Floor boards.		689.0	£ 25		9	✓		NOT IN USE	
3	W.C.	-	Wood throughout		2/240.0	£ 10		5			99 Demolished	
4	10 Connection Store	1903	Wood, zinc lined. Roof, zinc covered. Floor, concrete lead covered Earth traverse with brick retaining wall.		85505.0	£ 1740	1	10 1/2			36 Demolished & Rebuilt 63 Dem by Explosion No. No	New No. 36 F 
7	19 30 Engine House	1903	Wood. Roof, zinc covered Floor, concrete		6864.0	£ 475		1 1/2			No. 33 Demolished ✓	
5	Water Wardens and Police Hut	1881	Brick, Roof, slates Floor, boards.		1650.0	£ 70		10			NOT IN USE	
8	Clean Store	1885-6	Brick, matchlined throughout. Roof, brick and concrete tiles. Floor, boards, leather covered.		38257.0	£ 1435		9				
	Barge Cover Demolished, 06-7.	-	Corrugated iron on piles		49000.0	£ 150					Demolished, 06-7	










DEMOLISHED 1906.

Map No.	Description	When built	Construction	Dimensions	Cubic Contents	Cost of Buildings where known			Price per Cubic foot			Depreciation			Valuation			Remarks	No.
						£	s	d	£	s	d	£	s	d	£	s	d		
11 30	Gun cotton Store	1894-5	Wood, zinc lined, roof zinc covered. Floor, concrete, lead covered. Earth traverse with concrete retaining wall.		23069.0	750			8										
27	"	"	Earth traverse with brick retaining wall.		10148.0	374			8										
<del>22</del>	E.C.	1885-6	Wood, Roof, Slates		206.0	£ 5			6									Demolished 1908-9	
<del>23</del>	Clean Store	Part before 1880 part in 1885-6	Brick, match lined Roof, slates. Floor, boards, leather covered. Corrugated iron.		51726.0	£ 1295			6									Demolished 1908-9	
	Boat cover				3524.0	£ 10			3/4										
<del>25</del>	Store	1889-90	Brick, Roof, slates. Floor, boards. Concrete at (A)		10239.0	348			8									Demolished 1908-9	
24	E.C.	1896-7	Brick, Roof, corrugated iron, Floor, concrete.		217.0	£ 5			6										
25 28	Clean Store	1885-6	Brick, zinc lined throughout. Roof, zinc covered. Floor, leather and lead covered. Brick, match lined. Floor, leather covered. Roof, corr. iron.		54309.0	£ 2260			10										
	Boat cover		Brick, Roof, corrugated iron.		13501.0	£ 40			3/4										
26 30	Engine and Fan House	1885-6 m 26 1885-4 m 30	Brick and concrete. Roof, concrete, tiles. Floor, concrete.		78934.0	£ 1645			5									Invention Prof Stand.	



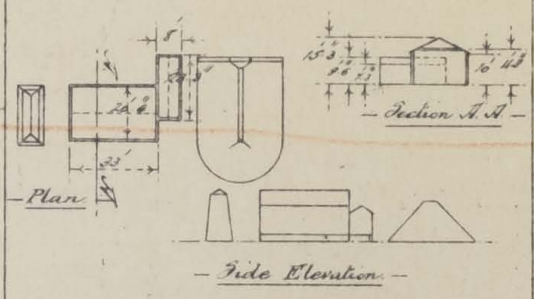


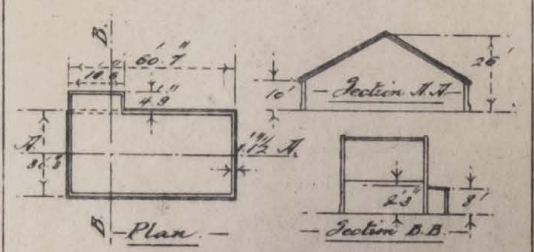



Ship No.	Description	When built	Construction	Dimensions	Cubic Contents	Cost of Buildings where known			Price per cubic foot			Depreciation			Valuation			Remarks	No.
						£	s	d	£	s	d	£	s	d	£	s	d		
<del>31</del>	<del>Engine driver flat</del>	1897-8	Wood, roof canvas covered, floor, boards		1452.0	£	35				6						<del>DEMOLISHED.</del>		
32	Clean Store	-	" " " " " "		1452.0	£	35				6								
34	Mixing House	1857-8	Wood, zinc lined, roof, slates Floor, concrete lead covered		20006.0	£	585				7						Original Building Demolished Rebuilt to new design 1942?		
	Shoe porch	-	Wood throughout, roof, zinc covered																
35	Bag Store	-	Brick, zinc lined, roof, slates Floor, concrete lead covered		1587.0	£	65				10								
36	Mixing House	1942?		NO DRS. AVAILABLE 															
<del>37</del>	<del>Concrete Bag Store</del>	<del>Before 1881</del>	<del>Brick, roof, slates Floor, asphalt covered</del>		<del>43084.0</del>	<del>£</del>	<del>1260</del>				<del>7</del>						<del>Demolished 1908-9</del>		
	Porch	1897-8	Wood, match lined, roof, zinc Floor, asphalt																
	Shoe Porch	-	Concrete																
37	STORE																		
<del>38</del>	<del>Store</del>	<del>Before 1821</del>	<del>Brick and Earth, roof, slates Floor, stone and brick</del>		<del>27413.0</del>	<del>£</del>	<del>685</del>				<del>6</del>						<del>Demolished 1908-9</del>		
38	FOREMAN'S OFFICE																	new Bldg 20x10	
<del>39</del>	<del>B.C.</del>		<del>Brick, roof, slates, floor, brick boards " " floor concrete</del>		<del>4715.0</del>	<del>£</del>	<del>80</del>				<del>4</del>						<del>Demolished 1908-9</del>		
41	E.C.	1897-8	Brick, roof, corrugated iron Floor, concrete		272.0	£	5				4 1/2								
42	Change House	1904-5	Wood, match lined throughout Roof, zinc, floor, lead covered		3418.0	£	85				6								



Map No	Description	When built	Construction	Dimensions	Cubic contents	Cost of Buildings where known			Price per cubic foot			Depreciation			Valuation			Remarks	No.
						£	s	d.	£	s	d.	£	s	d.	£	s	d.		
51	F.C.	1897-8	Brick. Roof, corrugated iron. Floor, concrete.		450-0	£	10				5 1/2								
52	Wash Water Settling House	1895-6	Wood, matchlined. Roof, canvas. Floor, concrete load covered		12285-0		208				4								
53	Mud Washing House	1895-6	Wood. Roof, canvas covered. Floor, concrete		2700-0		45				4								
56	Plumbers & Carpenters Shop	1874-5 1891-2 1893-6	Brick. Roof, zinc covered. Floor, boards		24710-0	£	310			1	3								
<del>57</del>	<del>F.C.</del>	<del>1897-8</del> <del>1903-4</del>	<del>Brick. Roof, corrugated iron. Floor, concrete.</del>	<del></del>	<del>453-0</del>	<del>£</del>	<del>10</del>				<del>5 1/2</del>							<del>Demolished</del>	
58	Store	1891-2	Wood, matchlined. Floor, boards		1748-0	£	50				4								
59	Office	1891-2	Brick, matchlined. Roof, brick & concrete, slates. Floor, boards		2121-0	£	80				9								
60	Ramp House	1904	Brick and Wood. Roof, slates. Floor, concrete		2138-0		26	18	8	1	3								
61	Water Tower Tank Cover Water Tank (10,000 gallons)	1896	Brick. Floors, wood & concrete. Wood. Roof felt covered. Iron throughout.		12125-0	£	505			1	10								



Map No.	Description	When built.	Construction	Dimensions	Cubic contents	Cost of Buildings where known	Price per cubic foot.	Depreciation	Valuation	Remarks.	No.
						£ s d	£ s d	£ s d	£ s d		
73	F. C.	1904	Brick. Roof, corrugated iron. Floor, concrete.		425.0	44 5 5	2 1				
<del>74</del>	<del>Engine &amp; Fan House</del>	<del>1879 and altered in 1904</del>	<del>Brick. Roof, slates. Floor, concrete.</del>	<del></del>	<del>6955.0</del>	<del>£ 175</del>	<del>6</del>			<del>demolished by explosion</del>	
<del>75</del>	<del>Gravelton Stove</del>	<del>1895 and re-erected on new site in 1901/2</del>	<del>Wood, zinc lined. Roof, zinc covered. Floor, concrete lead covered. Earth and concrete traverses.</del>	<del></del>	<del>11238.0</del>	<del>420</del>	<del>9</del>			<del>demolished by explosion</del> <b>REBUILT on same site new design</b>	
<del>76</del>	<del>Mixing House</del>	<del>About 1860</del>	<del>Wood, zinc lined roof. Floor, wood lead covered.</del>	<del></del>	<del>10121.0</del>	<del>£ 250</del>	<del>6</del>			<del>demolished</del>	
<del>76 B</del>	<del>Shoe porch</del>		<del>Wood, match lined. Roof, zinc covered. Floor, boards.</del>							<del>NEW Bldg. adjacent.</del>	
<del>76</del>	<del>Waste House</del>		<del>Brick &amp; earth.</del>							<del>demolished.</del>	
<del>77</del>	<del>Searchers Hut</del>	<del>1899</del>	<del>Wood. Roof, zinc covered. Floor, boards.</del>	<del></del>	<del>360.0</del>	<del>£ 5</del>	<del>3 1/2</del>				
78	Engine House	1895	Brick. Roof, slates. Floor, concrete.		38934.0	£ 975	6				
79	Shelling Room	Before 1821	Brick, match lined throughout. Roof, brick and concrete, slates. Floor, boards.		7072.0	£ 205	7				

73

~~74~~

~~75~~

~~76~~

~~76 B~~

~~76~~

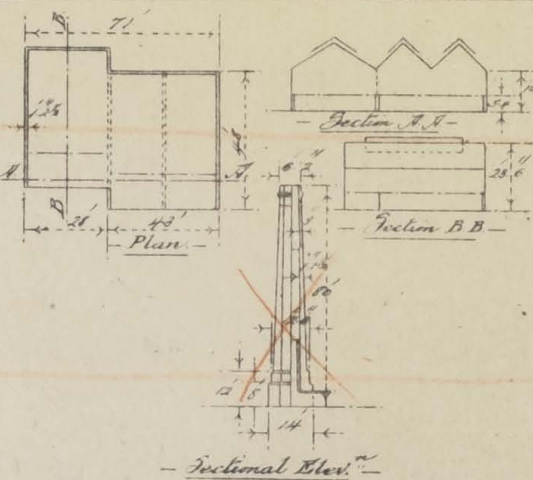

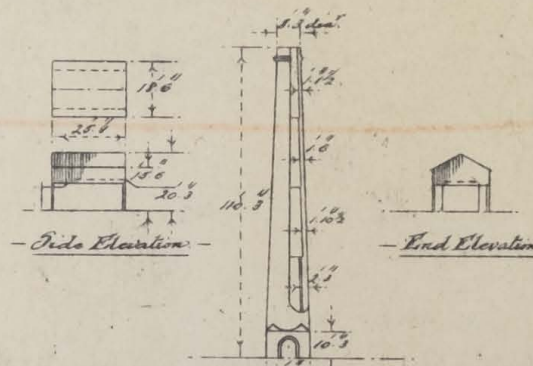





~~77~~

78

79

Gravelton Stove

Waste House

Map No.	Description	When built	Construction	Dimensions	Cubic contents	Cost of Buildings where known			Price per Cubic foot			Depreciation			Valuation			Remarks	No.
						£	s.	d.	£	s.	d.	£	s.	d.	£	s.	d.		
80	Boiler House	1895 6 1897 8 1903 4	Brick and Corrugated Iron. Roof, Corrugated Iron. Floor, Concrete and Stone.		76680.0	795			2 1/2									Demolished.	
81	Shaft (now disused)	1896	Brick		8300.0	£ 830			2 0									Demolished 1908-9	
82	Economiser Cover	1903 1904	Brick. Corrugated Iron.		5562.0 4635.0	835			3 0 8 1/2									Demolished	
83	Shaft	1903	Brick		6869.0	990			2 10 1/2										
84	Shifting Room Porch	Before 1896	Brick. Roof, slates. Floor, concrete & boards. Wood. Roof, lead covered. Floor, boards.		22814.0	£ 570			6										
85	H.C. Hot	1903-4	Brick. Roof, slates. Floor, concrete.		873.0	£ 15			4									Demolished	
86	Building Works Store	1903-4	Wood on brick, matchlined. Roof, canvas covered. Floor, brick.		1149.0	£ 15			3									Demolished	
87	H.C. & Sweeper Hut	1879	Brick. Roof, tiles. Floor, boards.		1845.0	£ 40			5									Demolished	

80

81 New building









83

84

85

86 Wooden Hut

87 H.C.

Map No.	Description	When built.	Construction.	Dimensions	Cubic contents.	Cost of Buildings where known. £ s. d.	Price per Cubic foot £ s. d.	Depreciation £ s. d.	Valuation £ s. d.	Remarks	No.
<del>88</del>	<del>Lobby</del>	<del>1879</del>	<del>Brick. Roof, tiles. Floor, concrete.</del>	<del></del>	<del>1845.0</del>	<del>E 40</del>	<del>5</del>			<del>demolished</del>	
<del>89</del>	<del>Credit Tray Hove</del>	<del>1879</del>	<del>Brick, matchlined &amp; zinc lined. Roof, zinc covered. Floor, leather &amp; lead covered. Brick, matchlined Floor, leather covered. Roof corr. iron.</del>	<del></del>	<del>42000.0</del>	<del>E 1575</del>	<del>9</del>			<del>demolished</del>	
91	Workman's H.										
89 ✓	Boat Cover Hose House	-	Brick. Roof, corrugated iron.		13301.0	E 40	3/4				
90	Boat House										
<del>92</del>	<del>H. C.</del>	<del>1879</del>	<del>Wood throughout.</del>	<del></del>	<del>72.0</del>	<del>E 5</del>	<del>1 5</del>			<del>demolished</del>	
92	See page 77.										
93	Blending House	1879	Wood, matchlined throughout. Roof, zinc covered. Floor, leather covered.		18514.0	E 500	6 1/2				
93	Shoe Room	-	Brick, matchlined throughout. Floor, boards. Earth traverse with brick and concrete retaining wall.								
<del>94</del>	<del>Boathouse (See page 77)</del>										
<del>94</del>	<del>Workshop (See page 77)</del>										
95	Fire Engine House	1902	Corrugated iron. Floor, concrete.		1492.0	E 20	3				
96	Dining Room	1861	Brick, matchlined throughout. Roof, shales. Floor, boards.		11661.0	E 240	5				











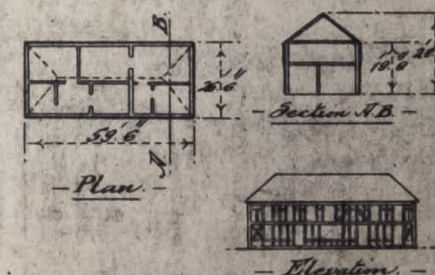




Map No.	Description	When built	Construction	Dimensions	Cubic Contents	Cost of Buildings where known			Price per Cubic foot	Depreciation			Valuation			Remarks	NEW BUILDING No.
						£	s	d.		£	s	d.	£	s	d.		
115	Paste Store Porch	1902 —	Brick, Red, slates. Floor, lead covered. Wood, matchlined throughout Roof, slates. Floor, lead covered.		11070.0	617	19	0	1	1 1/2						✓ L. 108.	
116	Gunpowder Breaking down House. Porches Traverse	1891 — Before 1870	Wood, matchlined. Roof, zinc covered. Floor, leather covered throughout. Brick and Earth		28385.0	E.	590			5					DEMOLISHED.		
118, 158	E. C.	Before 1886	Wood throughout.		239.0	E.	10			10					POOR SCRAP.		
119	Blank Cutting House Traverse	1902 Before 1880	Brick and Corrugated Iron. Roof, corrugated iron. Floor, Asphalt. Earth, with brick retaining walls.		7970.0		570			1	5				✓ L. 109.		
120	Traverse Motor Room	Before 1870 —	Brick and Concrete Floor, Concrete.		2160.0	E.	54			6				not used	L. 110.		
121	Magazine	1902	Brick. Roof, Willesden paper. Floor, Asphalt		1872.0	E.	50			6				no more	L. 111.		





Map No.	Description	When built	Construction	Dimensions	Cubic Contents	Cost of Buildings where known			Price per Cubic foot			Depreciation			Valuation			Remarks	No.
						£	s	d.	£	s	d.	£	s	d.	£	s	d.		
135	Spare Gear Room	1888	Wood, matchlined throughout. Roof, slates. Floor, leather covered.		10981.0	£	185.	.	.									Demolished 1908-9	
136	E.C.	1899 and extended 1904	Brick. Roof, slates. Floor, concrete.		772.0	£	20.	.	.										
137	Oven	1903	Uralite throughout.		54.0	£	5.	.	.		1	10							
138, 162, 216	Hydrant Hose House	1901-2 1903	Wood. Roof, slates. Floor, concrete.		5445.0	£	115.	.	.										no time ✓ with L.F. 139, L.F. 156, H.F. 9.
140	Electric Accumulator House	1904	Wood. Roof, slates & zinc. Floor, concrete.		860.0		39	7	4			11							✓ L. 121.
141	Cycle Shed	1902	Corrugated Iron.		559.0	£	10.	.	.										
142, 189	E.C.	1903	Brick. Roof, slates. Floor, concrete.		2613.0	£	90.	.	.										no time ✓ L. 144.
143	Forling House and E.C.	1889 -	Brick, matchlined throughout. Roof, slates, Floor, leather covered. Brick. Roof, slates. Floor, concrete.		4855.0	£	180.	.	.										no time ✓ L. 141.
144	Manager's Office and Laboratory	1897 and 1902	Brick and Wood, matchlined Roof, slates. Floor, boards.		42572.0	£	1596.	.	.										no time ✓ L. 122.



Map No	Description	When built	Construction	Dimensions	Cubic Contents	Cost of Buildings where known		Price per Cubic foot		Depreciation		Valuation		Remarks	No.	
						£	s.	d.	£	s.	d.	£	s.			d.
152	Incorporating 16 <sup>th</sup> Group A	1879	Brick and Wood. Roof, Zinc		40844.0	E	10210									
156	" " " G	1889	and slates. Floor, Asphalt													
160	" " " D	1868	" " " "													
167	Press Houses " C	1861	" " " "			13957.0	E	2800								
	Boiler Houses and Motor	"	Brick. Roof, zinc and slates. Floor, concrete and stone			62128.0	E	775								
	Chimney Shafts	"	Brick													
	Traverses	"	Concrete													
	Cabin, North end C	"	Wood. Roof, zinc. Floor, boards													
	" South end D	"	" " " "													
	Shed porch South end D	1906	Corrugated iron. Floor, boards			266.0	E	3 10								
	Track Shed & Covered Way N. end C	1898	Corrugated iron. Floor, boards		2831.0	E	36									
177	Cabin, South end, C	1896	Brick. Roof, slates. Floor, boards		1202.0	E	25									
	Traverses	1904-5	Concrete and Earth													
	Groups G & D															
154	Incorporating 16 <sup>th</sup> Group E	1867-8	Brick & Wood. Roof zinc. Floor, Asphalt		121,032.0	E	3026									
	Pump House	1877	Brick. Roof, slates & zinc. Floor, stone			3489.0	E	700								
	Chimney Shaft	"	Brick			14270.0	E	180								
	Accumulator House	"	Brick. Floor, stone & concrete													
	Open Gear Room	1902	Brick. Roof, zinc. Floor "													
	Cabin N. end demolished	1895	Wood. " " Asphalt													
	Traverse	"	Concrete													
	Water Tank (2000 gallons)	"	Iron throughout					80								
153	Paste Store	1877	Brick, matchlined throughout. Roof, slates. Floor, leather			2074.0	E	50								
	Traverse	1904-5	Concrete			1015.0	E	15								




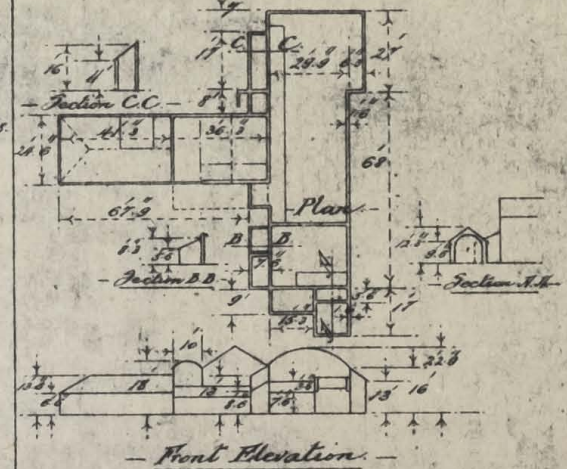



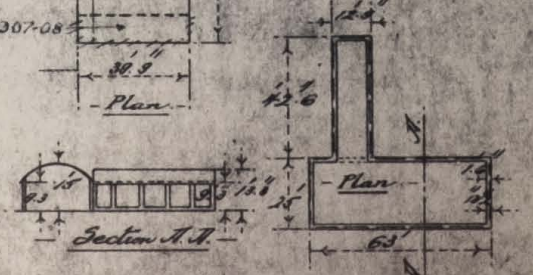
L 145. 1879  
 L 148. 1889  
 L 153. 1868  
 L 157. 1861

L 149.

Demolished





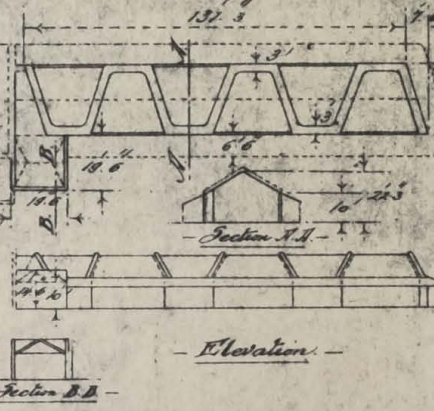

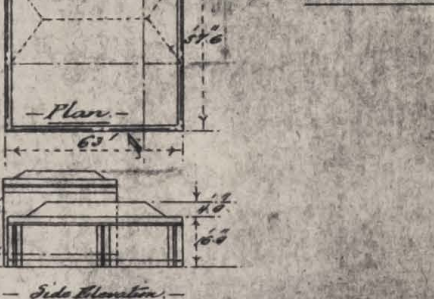





Map No.	Description.	When built.	Construction.	Dimensions.	Cubic Contents.	Cost of Buildings	Price	Depreciation	Valuation	Remarks.	No.
						where known	per				
						£ s d.	£ s d.	£ s d.	£ s d.		
168	Gasometer.	1889	Iron. Brick piers.								
169	Gasometer.	Before 1870	Iron throughout.		26,185.0	£ 525			4 3/4		
170	Gasometer.	-	Iron throughout.								
171	Gas Works Charcoal Burning Houses  Coal Shed.	-	Brick & Corrugated Iron. Roof, Corrugated Iron and slates. Floor, Stone.  Wood. Roof, slates. Floor, Concrete.		92,573.0	£ 1,930			5		L. 161
172	Gas Governor House.	-	Wood. Roof, slates. Floor, brick.		650.0	£ 15.			6		
173	Coal Store.	1891	Brick, Concrete & Corrugated Iron. Roof, Corrugated Iron. Floor, Concrete.		33,048.0	£ 690			5		L. 160
174	Boat Builders Shed.	1885	Corrugated Iron & Wood.		56,293.0	£ 460			2		L. 161
175	Charcoal Raking House.	1887	Brick. Roof, Corrugated Iron. Floor, concrete.		27,003.0	£ 450			4		L. 162

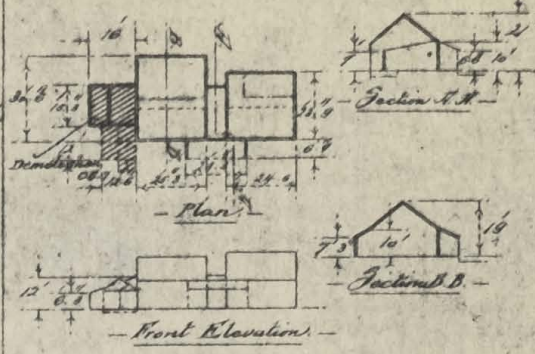
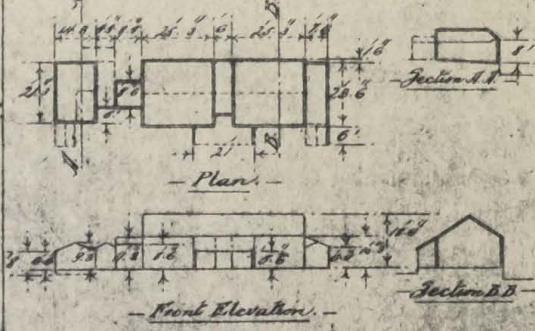




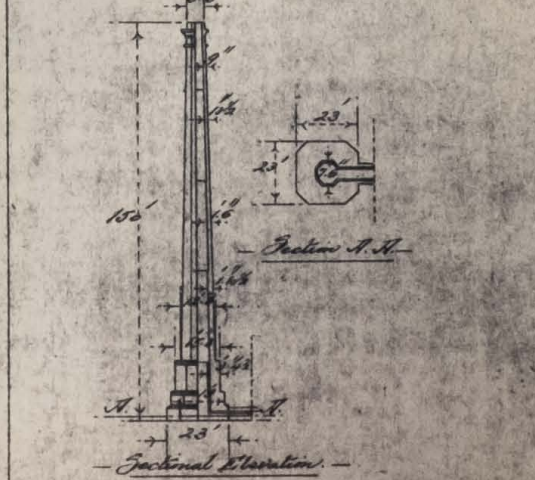
Demolished 1907-08



Map No.	Description	When built.	Construction	Dimensions	Cubic Contents	Cost of Buildings where known.		Price per Cubic Foot		Depreciation		Valuation		Remarks	No.
						£	s	d	£	s	d	£	s		
188 ✓	Hydrant Hose House.	Before 1886	Corrugated Iron throughout. Floor, Concrete.		471.9	£	9								
190	Magazine.	Before 1881	Brick, matchlined throughout. Roof, tiles. Floor, boards.		1952.0	£	48								
192 ✓	Experimental Stove	1857	Brick, matchlined throughout. Roof, slates. Floor, leather.		6338.0	£	185								
193	Gauge Cleaning House	---	---												
194	Press Houses, Group A	1857	Brick & Wood. Roof, zinc covered. Floor, Asphaltic.		88094.0	£	2202								
	Shoe Porch.	---	Brick. Roof, slates. Floor, boards.												
	Wade	1903	Corrugated iron.												
195	Machinery Shop	1857 extended 1881	Brick. Roof, slates & zinc. Floor, Wood.		88858.0	£	2221								
	Store	---	Brick. Roof, slates												
	Water Room.	1859.	Brick. Roof, zinc. Floor, concrete												
196	Lobby	1886	Wood. Roof, felt covered. Floor, boards.		1053.0	£	18								

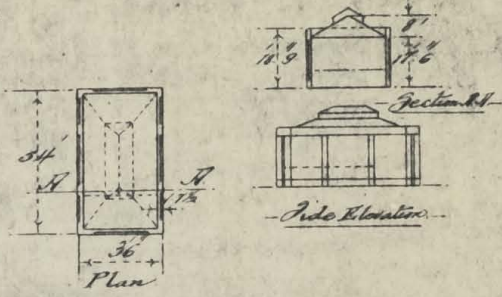



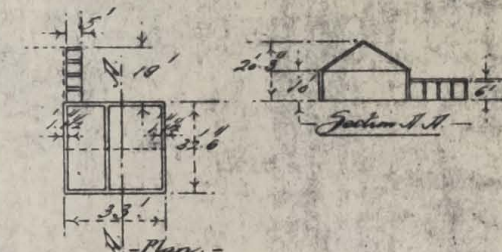

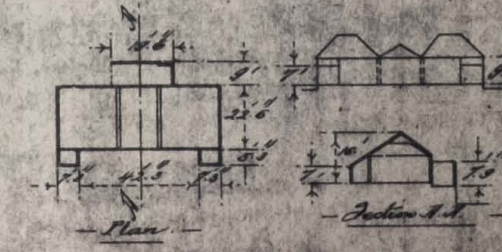
L170.  
L172  
L169.

LE168.








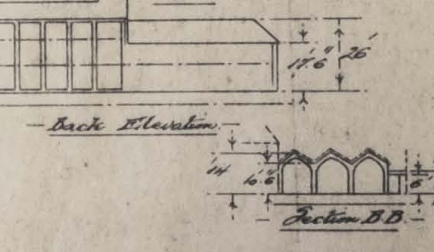

Map No	Description	When built	Construction	Dimensions	Cubic Contents	Cost of Buildings where known			Price per Cubic foot			Depreciation			Valuation	Remarks	No.
						£	s	d.	£	s	d.	£	s	d.			
197	Garwal Mills	Before 1783	Wood, Roof, Wood & Slates Floor, boards & leather covered		31570.0	£	658										
198*	Brimstone and Mixing Houses Shoe porch Demolished, 06-7	- - -	Wood, matchlined Roof, Slates Floor, boards & leather covered Wood, Roof, Zinc Floor, boards		30664.0	£	639									Demolished, 06-7 * Old 198 Demolished & E.C given same Number.	
198	E.C.	1907	Brick, Roof, Slates, Floor, concrete														
200	Sulphate Store Demolished, 06-7	Probably before 1773 Refined before 1870	Brick, matchlined throughout Roof, slates, Floor, boards		3381.0	£	113										Demolished, 06-7
201	E.C. Demolished, 06-7	Before 1870	Wood, Roof, Slates Floor, concrete		308.0	£	5										Demolished, 06-7
202	Sulphate Store	Before 1871	Brick, matchlined throughout Roof, tiles, Floor, boards		1658.0	£	55										
203	Chimney Shaft	1857	Brick		25341.0	£	1584										

no name  
L164

no name  
L174

Map No.	Description	When built	Construction	Dimensions	Cubic Contents	Cost of Buildings where known		Price per Cubic foot	Depreciation		Valuation		Remarks	No.
						£	s. d.		£	s. d.	£	s. d.		
204	Boiler House	1857	Brick. Roof, Slates & Glass. Floor, Stone.		47,628.0	E	1190							LE 176
205	Switchboard House	1902	Brick. Roof, Slates. Floor, Concrete.		9224.0	E	231							LE 177
206	Smiths Shop	1903	Brick & Corrugated Iron. Roof, Corrugated Iron. Floor, Concrete.		9555.0	E	160							LE 179
207	E.C.	1904	Brick. Roof, Slates. Floor, Concrete.		1025.0	E	26							L 178
208	Pipe Filters Shop & Store Bins	1905 --	Brick. Roof, Slates. Floor, Concrete. Brick. Roof, Corrugated Iron		17810.0		191 10 10							LE 180
209	Back drying Shed	1904	Corrugated Iron throughout.		1107.0		32 2 1							
210	Incorporating Mills Demolished, 06-7	Probably Before 1888	Wood. Roof, Wood & Corr. Iron. Floor, boards		18651.0	E	311						Demolished, 06-7	



Map No.	Description	When built	Construction	Dimensions	Cubic Contents	Cost of Building where known			Price per Cubic foot			Depreciation			Valuation			Remarks	No.
						£	s	d	£	s	d	£	s	d	£	s	d		
220	Coal Cover	1887	Corrugated Iron throughout Floor, brick		5520.0	52	11	4				27							
221	Visitor's Dangers Building Office	Before 1821	Brick. Roof, slates. Floor, boards		4472.0	E	93					5							
222	Drawing Office	-	Brick. Roof, slates. Floor, boards		12625.0	E	316					6							
223	Laboratory Store disused	-	-		1677.0	E	42					6							
224	Cordite Foreman's Office & Store	-	Brick. Roof, slates. Floor, boards		15401.0	E	385					6							
225	Boat House Demolished '05-6	-	Wood throughout		-	-	-	-	-	-	-	-	-	-	-	-	-	-	Demolished '05-6
226	Store Office	Before 1821	Brick. Roof, slates. Floor, boards		13582.0	E	339					6							A.S. 205 ✓
227	Stores E. C.	* Before 1821 & read out 1905  1897	Brick. Roof, slates. Floor, Concrete boards & Stone. Brick. Roof, Corrugated Iron Floor, Concrete		158627.0	E	3305					5							A.S. 203 ✓
228	Record Room	Before 1821	Brick. Roof, tiles. Floor, boards		14805.0	E	370					6							

A. 201. ✓

A. 202. ✓

A.S. 205 ✓

A.S. 203 ✓









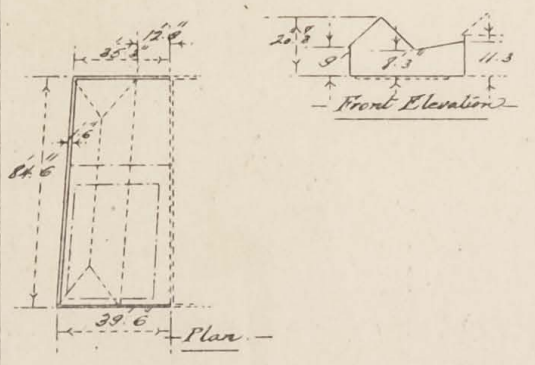
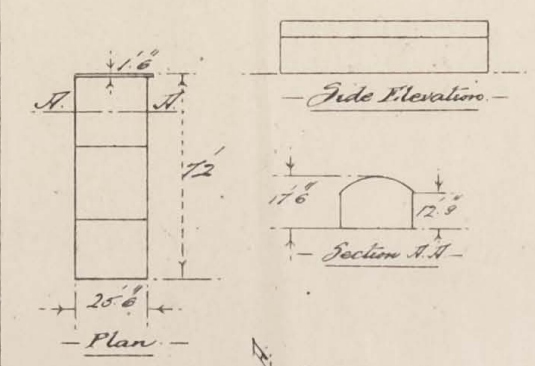
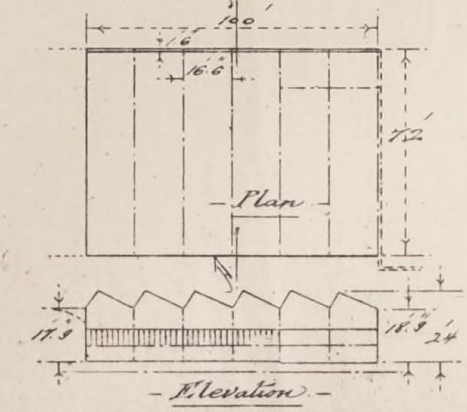
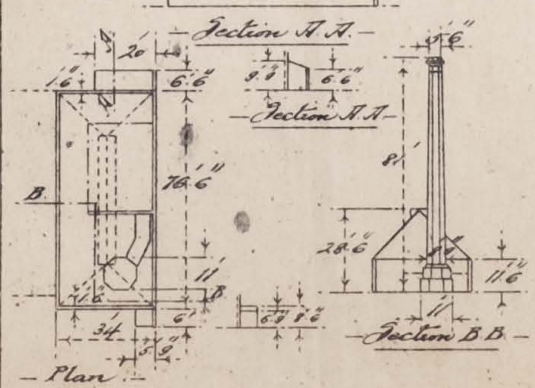
Map No.	Description	When built	Construction	Dimensions	Cubic Contents	Cost of Buildings where known			Price per cubic foot	Depreciation			Valuation			Remarks	No.
						£	s	d		£	s	d	£	s	d		
245	Timber Store Office Battery Store	Before 1821 - 1906-7	Brick Roof, Slates. Floor, Concrete. Wood		51,079.0	£	958	.	4 1/2						A 234 ✓		
246	Over	Before 1886	Willesden paper throughout Floor, Concrete		565.0	£	11	.	5								
247	Cover	1890	Corrugated Iron		6983.0	£	58	12	2								
248	Boat builders Shed	Before 1886	Wood & Corrugated Iron Roof, Zinc		8978.0	£	112	.	3						AB. 243		
249	Paint Store	-	Corrugated Iron throughout Floor, Concrete		853.0	£	11	.	3								
250	Store Lean to	Before 1821	Brick Roof, Slates Wood, Roof, Tiles		12754.0	£	266	.	5								
251	Police Station Library & Billiard Rm Cookhouse, Washhouse & H.C.	Ground floor Before 1821 & extensions since	Brick Roof, Slates Floors, boards Brick Roof, Slates, Floor, Concrete		77,756.0	£	1944	.	6						A 238 ✓ A 268 - wrong		





Map No.	Description	When built	Construction	Dimensions	Cubic Contents	Cost of building where known		Price per cubic foot		Depreciation		Valuation		Remarks	No.
						R	L	R	L	L	R	L	R		
273	Outhouse D. B. O's Quarters	Before 1886	Brick. Roof, slates. Floor, concrete.		4011.0	E	67							no price AS. 281.	
274	Extracting House	1855	Brick & Wood. Roof, canvas Floor, stone.		24776.0	E	516								
275	Ammonia Rectale House	1885	Brick, matchlined throughout. Roof, slates. Floor, Asphalt.		7290.0	E	182							no price AS. 280.	
276	Hospital	1895	Brick. Roof, tiles. Floor, boards & concrete.		32432.0		1210	8						H 26. no price	
277	Coal Shed	1895	Brick. Roof, tiles. Floor, concrete.		741.0	E	19								
	Lean-to	-	Wood. Floor, concrete.												
278	Sulphate Store & Melting House	1816	Brick. Roof, tiles. Floor, Stone, Concrete & boards		65552.0	E	1229							A. 278.	
279	Crystallizing House	-	Brick. Roof, tiles Floor stone.											A. 279	no price
280	"	1871	Wood. Roof, slates & glass. Floor, concrete.		179838.0	E	3747							No NUMBER	
281	Grough Store	1816	Brick. Roof, slates. Floor, stone.											A. 277.	



Map No.	Description.	When built.	Construction.	Dimensions.	Cubic Contents	Cost of Buildings where known.		Price per Cubic foot.		Depreciation.		Valuation.		Remarks.	No.
						£	s	d	£	s	d	£	s		
289.	Shed.	1872	Corrugated Iron.		1021.0	£	17	.	.	4					
290.	W.C.	1872	Brick. Roof Slates. Floor, Concrete.		410.0	£	14	.	.	8				H.S. 32	} house
291.	Acetate of Lime & Drum Store.	Before 1821	Brick & Wood. Roof, slates, & Corrugated Iron. Floor, Concrete.		43968.0	£	916	.	.	5			H.S. 31		
292.	Recreation Hall.	1872	Corrugated Iron throughout. Floor, Stone & Concrete.		29376.0	£	490	.	.	4					
293.	Recreation Hall.	1872	Brick & Wood. Roof, corrugated Iron, Wood & glass. Floor, boards & concrete.		172800.0	£	4320	.	.	6					
294.	Drum Store 07.1.  Culmney. Lean to.	Before 1821.	Brick. Roof, tiles. Floor, concrete.		59823.0	£	1496	.	.	6				A.E. 275	} house
		1872	Brick.		4640.0	£	464	.	.	2	0				
		-	Wood. Roof, slates.		1381.0	£	17	.	.	3					







Map No.	Description.	When built.	Construction	Dimensions	Cubic Contents	Cost of Building where known			Price per Cubic foot			Depreciation			Valuation			Remarks	No.
						£	s	d	£	s	d	£	s	d	£	s	d		
317, 318. 319, 320.	Cottages 6 Rooms.	1865	Brick, Roof, Slates Floor, boards.		45,494-0	£	854	-	-	-	4	-	-	-	-	-	-	-	
321, 322 323, 324.	Cottages 6 Rooms.	1866	Brick, Roof, Slates. Floor boards.		43,886-0	£	822	-	-	-	4	-	-	-	-	-	-	-	
325, 326. * 327.	Cottages 6 Rooms * 8 Rooms * Demolished 06-7.	Before 1821.	Brick, lath & plaster Roof, slates & tiles. Floor boards, brick & concrete		11,893-0	£	198	-	-	-	4	-	-	-	-	-	-	Demolished 06-7	
328.	Shed	-	Wood Roof, tiles & slates. Floor, concrete.		1091-0	£	18	-	-	-	4	-	-	-	-	-	-	-	
329.	Scullery	-	Brick, Roof, slates. Floor, brick.		1091-0	£	23	-	-	-	5	-	-	-	-	-	-	-	
330.	Shed	-	Brick, Roof, Slates. Floor, brick		741-0	£	14	-	-	-	4	-	-	-	-	-	-	-	
331.	Cottage 8 Rooms.	Before 1820.	Brick, Roof, tiles. Floor, boards & stone.		18,877-0	£	315	-	-	-	4	-	-	-	-	-	-	-	

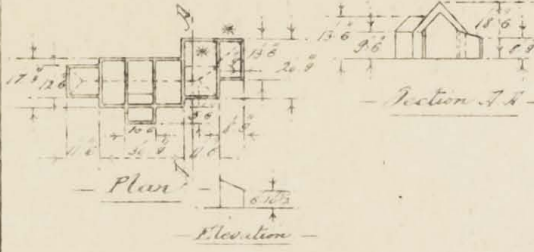




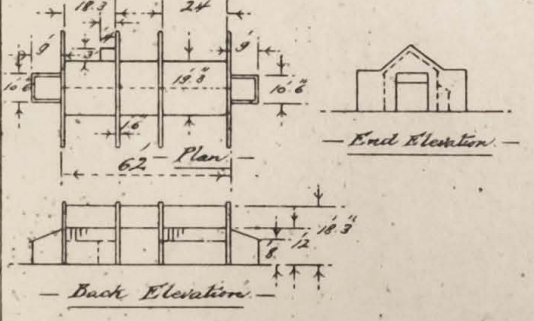

Map No.	Description	When built	Construction	Dimensions	Cubic Contents	Cost of Buildings where known			Price per Cubic foot			Depreciation			Valuation	Remarks	No.
						£	s	d	£	s	d	£	s	d			
332	Shed & W.C.	Before 1820	Brick. Roof, tiles. Floor, concrete & brick		1909 - 0"	E	32	-	-	4							
333	Gardeners Quarters	"	Brick Roof tiles Floor boards		25,145 - 0"	E	419	-	-	4							
334	Stable	"	Brick Roof slates Floor, brick & concrete		13,741 - 0"	E	229	-	-	4							
335	Harness Room & Washhouse	"	Brick Roof slates Floor, concrete		5792 - 0"	E	97	-	-	4							
336	Superintendents Quarters	Old part before 1820 Extended 1893	Brick Roof, tiles & slates Floor boards & concrete		60,274 - 0" old part 64,274 - 0" new part	E	1507 2411	-	-	6 9							
337	W. C.	1893	Brick. Roof, slates Floor, concrete		184 - 0"	E	9	-	-	0							
338	Cottage 6 Rooms	Before 1821	Brick. Roof, slates Floor, boards		12,541 - 0"	E	209	-	-	4							







Map No.	Description.	When built.	Construction.	Dimensions.	Cubic contents.	Cost of Buildings where known.			Price per Cubic foot.			Depreciation.			Valuation.			Remarks.	No.
						£	s	d	£	s	d	£	s	d	£	s	d		
383.	Covered Way. Demolished, 06-7.	1886	Corrugated Iron.		45514.0	£	285				12							MS. 305 Demolished, 06-7.	✓
384.	Clean Store.	1886	Brick, matchlined throughout. Roof, slates. Floor, boards.		5635.0	£	141				6							MS. 306.	✓
385.	Acetone Store Demolished, 06-7.	Before 1886. and 1887	Brick. Roof, slates & Corrugated Iron. Floor, Stone & Concrete.		95764.0	£	2394				6							MS. 307.	✓
386.	Chimney.	Before 1887	Brick.		3920.0	£	441				2	3						MS. 308.	✓
387.	Acetone Store. Porch * (Demolished, 06-7)	1859	Brick & Wood. Roof, Wood, Floor, boards. Brick. Roof, Cor. Iron. Floor, Concrete. Wood throughout. Floor, boards.		57206.0	£	1430				6							MS. 309.	✓

Map No.	Description	When built	Construction	Dimensions	Cubic contents	Cost of Buildings where known		Price per Cubic foot	Depreciation		Valuation		Remarks	No.
						£	s		d	£	s	d		
388	Water Wardens House Dining Room Fire Engine House	Before 1821 Before 1850	Brick, Roof, Slates Floor, boards Floor, concrete		13520.0	£	333						M. 311 ✓	
389	Washhouse	Before 1886	Brick, Roof, Slates Floor, stone		1238.0	£	21							
390, 391	Magazines Demolished, 05-6	Before 1821	Brick, matchlined throughout Roof, slates. Floor, boards		7911.0	-	-	-	-	-	-	-	Demolished, 05-6	
392	Magazine	-	Brick, matchlined throughout Roof, slates. Floor, boards		4066.0	£	135						M. 312 ✓	
393	Magazine	1889	Brick, matchlined throughout Roof, slates. Floor, boards		9261.0	£	414	19					M. 313 ✓	
394	Incorporating Mill & Corn House	1894	Brick & Wood, matchlined throughout. Roof, zinc covered Floor, boards		24036.0	£	601							
395	Granulating House Wheel House	Before 1870	Brick, matchlined throughout Roof, slates. Floor, leather covered Wood, Roof, Corrugated Iron		12623.0	£	369							



Map No.	Description	When built	Construction	Dimensions	Cubic Contents	Cost of Buildings where known			Price per Cubic foot			Depreciation			Valuation	Remarks	No.
						£	s.	d.	£	s.	d.	£	s.	d.			
396	Traverse (Old Store)	Before 1860	Brick, Roof, slates. Floor, concrete.		8033.0	£	168	.	.					5			
397	Picnic Blending House	1889	Wood, matchlined throughout. Roof, zinc. Floor, leather covered.		8147.0	£	153	.	.					4½			
398	Gear Room	1871	Brick, Roof, slates. Floor, boards.		13622.0	£	284	.	.					5			
399	Press House  Traverses	-  -	Wood, matchlined. Roof, zinc covered. Floor leather covered.  Brick & earth.		6904.0	£	144	.	.					5			
400	Drum House  Traverse	-  -	Wood, matchlined. Roof, zinc covered. Floor, leather cover.  Brick & earth.		32640.0	£	680	.	.					5			
401	Loading Stage	1900	Corrugated Iron.		920.0	£	15	.	.					4			

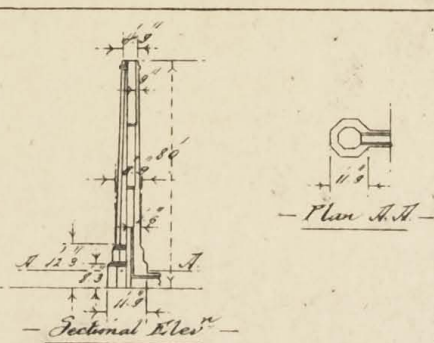
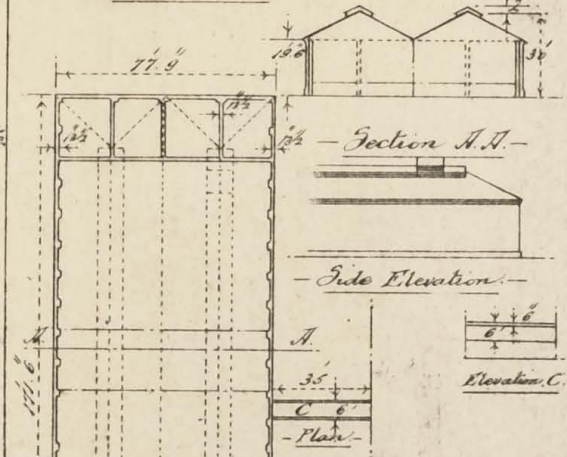



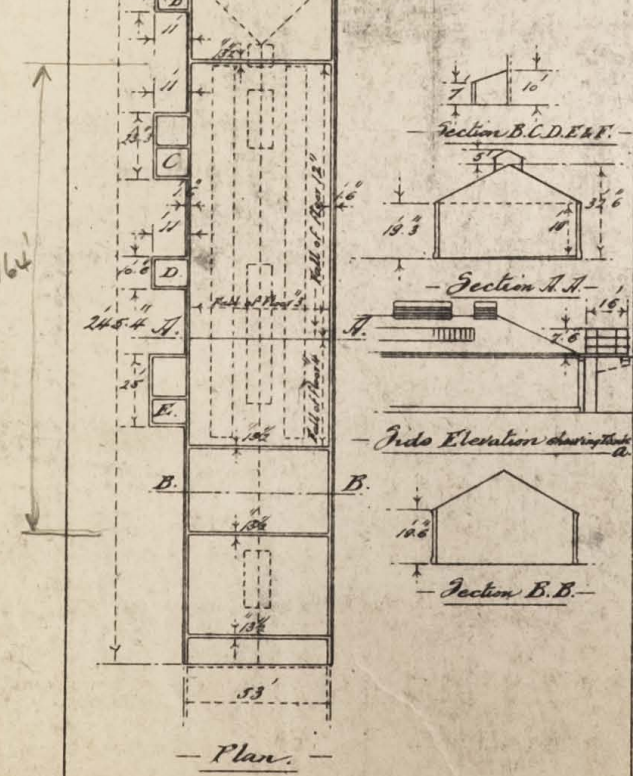


Map No.	Description	When built	Construction	Dimensions	Cubic Contents	Cost of Buildings where known			Price per Cubic foot	Depreciation			Valuation			Remarks	No.
						£	s	d.		£	s	d.	£	s	d.		
406	Carpenters Shop & Office (B.W. Dep't)	1905	Wood. Roof, tiles. Floor, boards. Wood, matchlined. Roof, canvas. Floor, boards.		5358.0	E	67	.	3							M. 323 ✓	
407	B.W. Dep't Store.	--	Brick & Corrugated Iron. Roof, Corr. Iron. Floor, Concrete		9526.0	E	159	.	4								
408	B.W. Dep't Store.	1897	Brick & Wood. Roof, slates. Floor, Concrete.		3257.0		59	10	3	4 1/2							
409 & 449 522	E. C.	1903	Brick. Roof, slates. Floor, Concrete.		2308.0	E	58	.	6							No. 522 G 404 G 427 ✓ No NUMBER FOR 522	
410	Power House	1905-6	Brick, with Steel frame. Roof, slates. Floor, Cast Iron plates & Concrete.		249289.0		4512	.	4 1/2							GE 403 ✓	
411	Shifting Room	1904	Corrugated Iron throughout. Floor, Concrete.		1107.0		32	2	1	7						No. 522 G.E. 405 ✓	
412	Fan House	1903	Corrugated Iron & Wood. Floor, Concrete.		7124.0	E	119	.	4							No. 522 G.E. 406 ✓	
413	Plumbers Shop	1888	Brick. Roof, slates. Floor, Concrete.		27000.0	E	507	.	4 1/2							G.E. 407 ✓	

Map No.	Description.	When built.	Construction.	Dimensions.	Cubic Contents.	Cost of Buildings where known.			Price per Cubic foot.			Depreciation.			Valuation.			Remarks.	No.
						£	s	d.	£	s	d.	£	s	d.	£	s	d.		
414	Office.	Before 1890 & erected on present site 1892	Wood. Roof, canvas covered. Floor, boards.		972.0	E.	20	.	.	5								no name GE 408.	
415	Engine Room (Coal Elevator.)	1903	Brick. Roof, slates. Floor, concrete.		2516.0	E.	63	.	.	6									
416	Chimney.	1902-3	Brick.		44,795.0		2168	.	.	11 1/2									
417, 418	Economiser Chamber. Cover over Economiser.	-	Brick. Corrugated iron throughout.		53,760.0		2594	.	.	11 1/2									
419	Boiler House	-	Brick, corrugated iron & wood, with steel frame. Roof, slates. Floor, stone, concrete & cast iron plates.		303,599.0		4571	.	.	3 1/2									
420	Engine House. (Coal Elevator.)	1903	Corrugated iron. Floor, concrete.		1091.0	E.	18	.	.	4								no name G. 413.	
421	Painting Room (Plumbers)	1892	Brick. Roof, slates. Floor, concrete.		3126.0		125	.	.	9 1/2								G 411	

} GE 409.



Map No.	Description	When built	Construction	Dimensions	Cubic Contents	Cost of Buildings where known		Price per Cubic foot.	Depreciation		Valuation		Remarks	No.
						£	s. d.		£	s. d.	£	s. d.		
426.	Chimney.	1898-9	Brick.		4'092.0"	£	409	2	0					
427	Pulping & Moulding Room.	1888	Brick. Roof, slates. Floor, Asphalt & concrete		390798.0"	£	8142	5					G. 418 ✓	
	Covered Way.	--	Corrugated iron. floor, boards.											
	Pump House *	--	Floor Concrete											
	Box House.	--	" "											
428.	Chimney (partly demolished) 00-7.	--	Brick.		2450.0"	£	243	2					Partly demolished 00-7.	
429	Nitrating House.	--	Brick. Roof, slates. Floor, blue brick.		383,933.0"	£	8000	5					G. 422.	
	Water Tank (10,000 gallons) & Girders.		Iron throughout.				130							
	Pump & Fan House.	1888 & 1902	Brick. Roof, slates. Floor, blue brick.											
	Weighing Room.	1888	Floor, blue brick.											
	Drying Room.	--	Floor, concrete.											
	Fan Room.	--	" "											

739  
37  
1109

G. 422.  
none

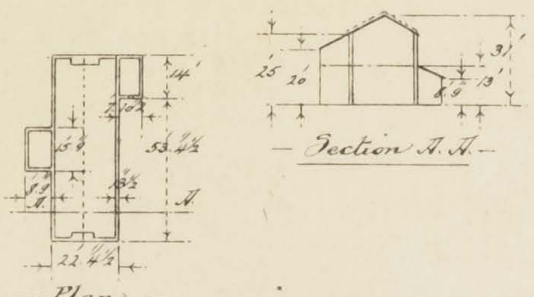





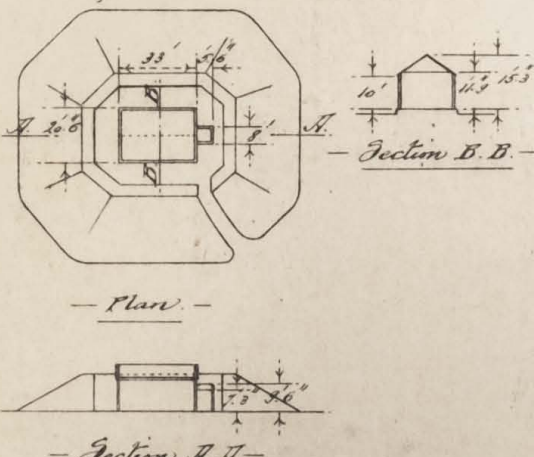




Map No.	Description.	When built.	Construction.	Dimensions.	Cubic contents.	Cost of Buildings where known.		Price per Cubic foot.		Depreciation.		Valuation.		Remarks.	No.
						£	s d.	£	s d.	£	s d.	£	s d.		
435.	Sulphuric Acid Concentration Plant.	1904 5	Brick. Roof, slates. Floor, concrete & blue brick.		266,303.0									G. 441 ✓ Prov IV	
	Platform for Ceric Condensers.	-	Wood, on blue brick piers.		74,939.0	7037		5							
436.	Nitric Acid Concentration Plant.	-	Brick. Roof, slates. Floor, blue brick on concrete.		328,394.0	5850		4 1/2						G. 443 ✓	
437.	Tower for Acid Tanks.	-	Brick. Floor, concrete & blue brick.		11,851.0	412		8 1/2							



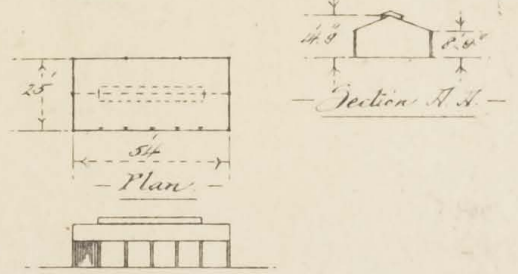


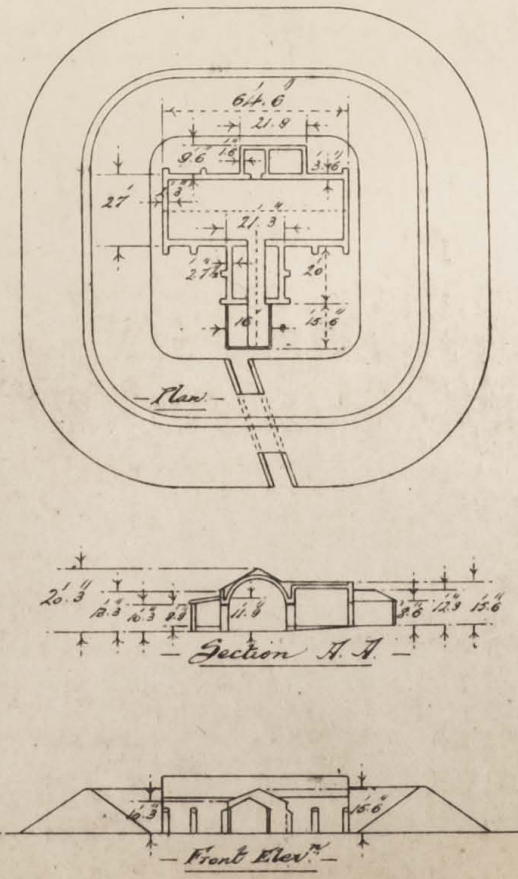


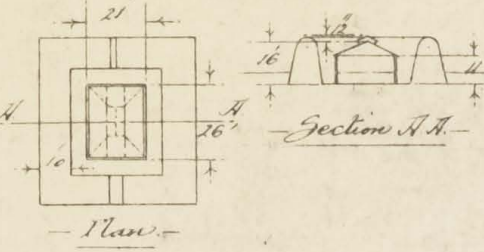
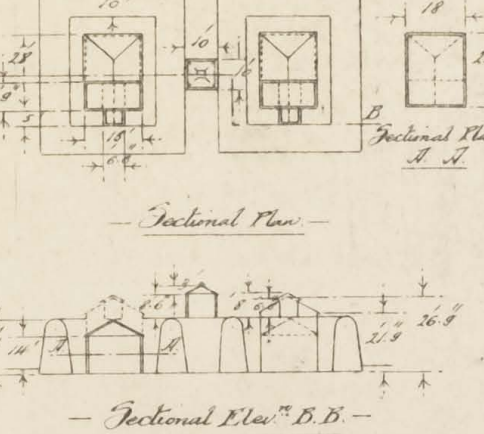


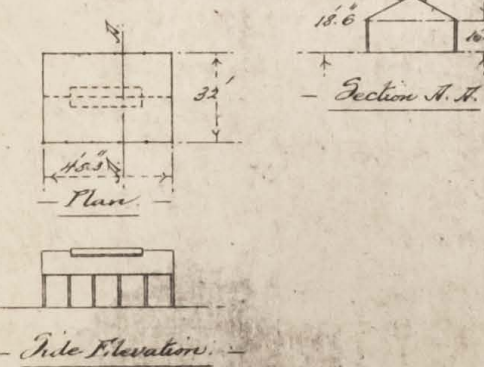


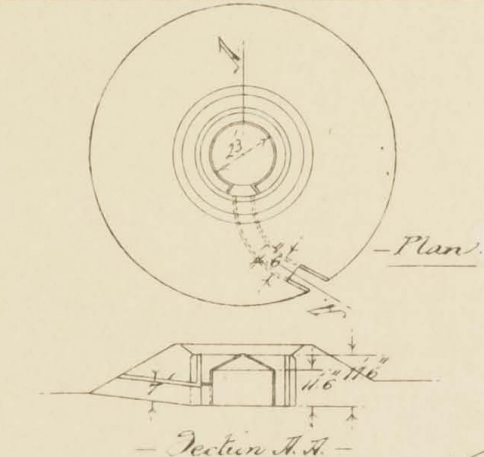
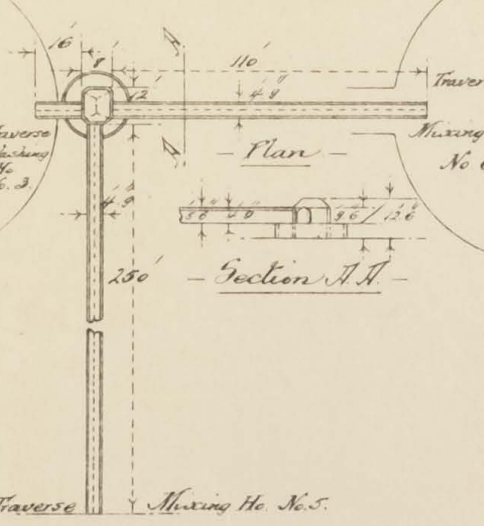

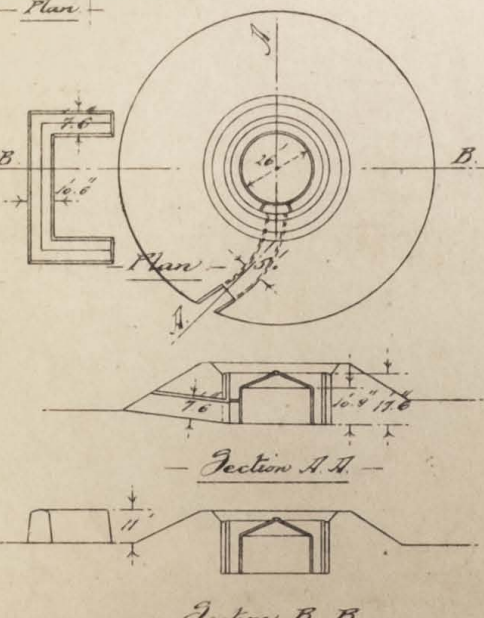
Map No.	Description.	When built.	Construction.	Dimensions.	Cubic contents.	Cost of Buildings where known.			Price per Cubic foot.			Depreciation.			Valuation.			Remarks.	No.
						£	s.	d.	£	s.	d.	£	s.	d.	£	s.	d.		
445.	E.C.	1888	Brick. Roof, slates. Floor, concrete.		2097.0	£	52	.	.	.	6							G. 426. <i>where</i>	
446.	Refrigerating House.	1895	Brick. Roof, slates. Floor, concrete.		14762.0	£	369	.	.	.	6							GE. 424. ✓	
447.	Motor Spare House.	1892	Brick. Roof, slates. Floor, concrete.		5684.0	£	142	.	.	.	6								
448.	Hydrant Hose House.	1902	Wood. Roof, slates. Floor, concrete.		1053.0	£	18	.	.	.	4								
450.	Packing House.	-	Brick. Roof, slates. Floor, Asphalt.		20106.0	£	503	.	.	.	6							G 421. ✓	
451.	Folding House.	-	Brick. Roof, slates. Floor, concrete.		3120.0	£	78	.	.	.	6								
452.	House (Motor Wagon)	1905	Brick. Roof, slates. Floor, concrete.		4941.0		135	12	9		6½							G 415. ✓	
453.	Cycle Shed.	1904	Corrugated Iron.		455.0	£	9	.	.	.	5								
454.	Office & Laboratory.	-	Brick. Roof, slates. Floor, boards.		29261.0		800	.	.	.	6½							N 500. ✓	

Map No.	Description.	When built.	Construction.	Dimensions.	Cubic contents.	Cost of Buildings where known.			Price per Cubic foot.	Depreciation.			Valuation.			Remarks.	No.
						£	s.	d.		£	s.	d.	£	s.	d.		
455,521.	Shifting Room.	1904	Brick. Roof, slates. Floor, boards & concrete.		100,991.0	2858			6 3/4							No. NUMBER <b>N.559.</b> ✓ w/price	
456.	Shed (demolished 05-6)	-	Wood. Roof, canvas covered. Floor, boards.		-											Demolished, 05-6. <b>G 414</b> ✓ w/price	
457.	Instrument Room.	1887	Brick. Roof, zinc covered. Floor, boards.		6635.0	166			6							M 329 ✓	
458	E. C.	1904	Brick. Roof, slates. Floor, concrete.		270.0	7			6							<b>N. 503.</b> ✓	
459.	Guncotton Stove. (Experimental)	1888	Willesden paper. Floor concrete.		772.0	13			4							<b>M. 336.</b> ✓	
460.	Dry Guncotton Magazine.	1904	Brick. Roof, zinc. Floor, Asphaltic. Earth Traverse.		1614.0	90			1 1								
461.	Guncotton Stove.  Traverse.	About 1895  --	Wood, zinc lined. Roof, zinc covered. Floor, concrete, lead covered.  Earth & corrugated iron.		11,198.0	600			1 1							<b>M 325.</b> ✓	
462.	Engine House.	1895	Wood. Roof, felt covered.		2783.0	70			6							<b>M. 324.</b> ✓	
463.	" "	1894	Floor, concrete.													M 337 ✓	

Map No.	Description.	When built.	Construction.	Dimensions.	Cubic contents.	Cost of Buildings where known.		Price per Cubic foot.		Depreciation.		Valuation.		Remarks.	No.
						£	s	d.	£	s	d.	£	s		
464.	Guncotton Store.	1894	Wood, zinc lined. Roof, zinc covered. Floor, concrete, lead covered. Earth traverse.		11,967.0	£	299	.	.	6					
465.	Cordite Magazine.  Shoe Room. Truck Torch. Traverse.	1892	Brick, Roof, Slates. Floor, leather covered. -- Floor, boards. -- Wood, Roof, Slates. Earth.		28,912.0	£	844	.	.	7				M. 342 ✓	
466.	Dry Guncotton Lacking House. Torch.  Traverse.	About 1895	Brick, Roof, Zinc covered. Floor, Asphalt. Wood, Roof, Zinc covered. Floor, lead covered. Earth.		9,931.0	£	289	.	.	7				M. 345 ✓	
467.	Armoury (demolished) c.s. 6.	-	Wood, Roof, Canvas. Floor, boards. Floor, concrete.		-										
468.	Store.	1887-8	Corrugated Iron & Wood. Roof, Cor. Iron, Canvas covered. Floor, concrete.		6,143.0	£	102	.	.	4				M. 339 ✓	

No.	Description.	When built.	Construction.	Dimensions.	Cubic Contents.	Cost of Buildings where known.			Price per cubic foot.			Depreciation.			Valuation.			Remarks.	No.
						£	s	d	£	s	d	£	s	d	£	s	d		
469.	Store (demolished 05-06)	-	Wood. Roof, felt covered. Floor, boards.		-													Demolished, 05-06	
470	Magazine (demolished 05-05)	-	Wood. Roof, felt covered. Floor, leather covered.		-													Demolished, 05-05	
471.	Gun Shed.	1887-8	Corrugated Iron & Wood. Floor, Concrete.		17,551.0	E	293			4								M 346 ✓	
472.	Cell.	1887-8	Wood & Iron. Roof, Concrete. Floor, Stone & Concrete. Earth traverse.		3,003.0	E	75			6									
473.	Shed.	1890	Iron & Wood. Roof, felt covered. Floor, boards.		231.0	E	6			6									
474.	Cordite Magazine.  Shoe Porch. Truck Porch. Traverse.	- - - -	Brick, match lined throughout. Roof, brick & concrete, tiles. Floor, Asphalt. Roof, Concrete. Floor, boards. Wood. Roof, Zinc covered. Earth.		45,433.0		2268	9		1	0								N. 545. no more

No.	Description.	When built.	Construction.	Dimensions.	Cubic Content.	Cost of Buildings where known. £ s. d.	Price per cubic foot. £ s. d.	Depreciation. £ s. d.	Valuation. £ s. d.	Remarks.	No.
475.	Alter Separating House.  Traverse.	1891	Wood, matchlined. Roof, Canvas covered. Floor, boards & Concrete.  Brick.		8463.0	E 141 . .	4				
476, 477.	Nitrating Houses.  Charge House.  Traverses.	1891	Wood, matchlined. Roof, Zinc covered. Floor, boards & lead covered.  Wood, matchlined. Roof, Zinc covered. Floor, lead covered.  Brick.		23048.0	E 576 . .	6			N 543 ✓ No NUMBER.	
478.	Water Tower.  Water Tank, (10000 gallons)	1891	Brick. Floor, boards & Concrete. Iron throughout.		8168.0	E 204 . .	6			N 541 ✓	
479.	Glycerine Store.	-	Wood, matchlined throughout. Roof, felt covered. Floor, boards		5376.0	E 90 . .	4				
480, 481, 482.	Acetone Store.	1892	Corrugated Iron. Roof, Slates, & Zinc. Floor, concrete.		69604.0	E 1158 . .	4			NS 550. NS 551. NS 552.	

No.	Description	When built	Construction	Dimensions	Cubic Contents	Cost of Buildings where known. £ s d.	Price per cubic foot. £ s d.	Depreciation. £ s d.	Valuation. £ s d.	Remarks	No.
483.	Washing House	1894	Wood, matchlined. Roof, Zinc covered. Floor, lead covered. Earth traverse with brick & concrete retaining wall.		8904.0	E 185	5			N. 544 ✓	
484.	Junction House Covered Way.	- "	Wood. Roof, felt covered. Floor, tar paving. - " Wood. Roof, felt covered. Floor, tar paving.		10557.0	E 176	4				
485.	Mixing House Porch.	- "	Wood, zinc lined throughout. Roof, zinc covered. Floor, lead covered. - " Wood, matchlined. Floor, boards. Brick traverse.		11554.0	E 241	5			N. 548. ✓	
486.	Mixing House Traverse. Traverse (West Side)	- " - " - "	Wood, zinc lined throughout. Roof, felt covered. Floor, lead covered. - " Earth traverse with brick & concrete retaining wall. - " Brick.		9041.0	E 189	5			N. 549. ✓	





No.	Description.	When built.	Construction.	Dimensions.	Cubic Contents.	Cost of Buildings where known.		Price per cubic foot.		Depreciation.		Valuation.		Remarks.	No.
						£	s.	d.	£	s.	d.	£	s.		
493	Bulbs.	1887	Concrete & Wood. Roof, timber, iron & tar paving. Earth traverse.		46075.0	£	960		5					M. 350. ✓	
494	Greencliff Stove.	1892	Wood, Zinc lined throughout. Roof Zinc covered. Floor, concrete, lead covered. Earth traverse with brick retaining wall.		10332.0	£	344		8					M. 351. ✓	
495	Engine House.	"	Wood. Roof, felt covered. Floor, concrete.		1100.0	£	23		5						
496	Cordite Tray Stove.	1896	Brick, Zinc lined throughout. Roof, Zinc covered. Floor, lead covered.		9141.0	£	229		6					M. 352. ✓	
	Porch.	"	Wood. Roof, Zinc covered.												
497	E. C.	1903	Brick. Roof, slates. Floor, concrete.		602.0	£	15		6						



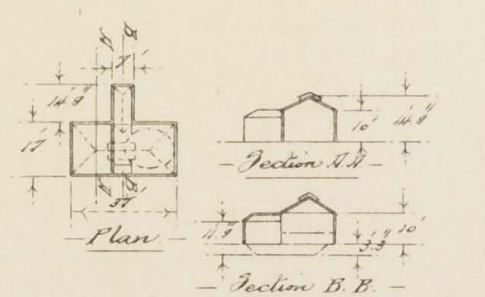


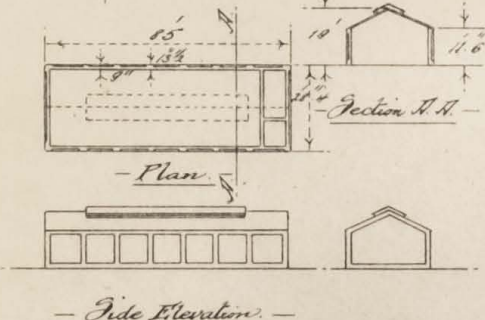
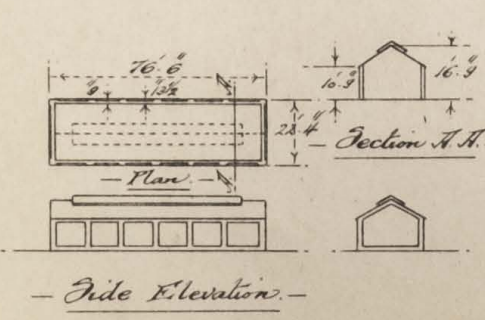
No.	Description.	When built.	Construction.	Dimensions.	Cubic contents.	Cost of Buildings where known.			Price per cubic foot.			Depreciation.			Valuation.			Remarks.	No.
						£	s	d.	£	s	d.	£	s	d.	£	s	d.		
498.	Switchboard House.	1903	Corrugated iron throughout. Floor, concrete.		5640.0	157	.	.	6	$\frac{3}{4}$									
499.	Boiler House.	--	Brick & Corrugated iron. Roof, slates. Floor, concrete & stone.		66309.0	1499	.	.	5	$\frac{1}{2}$									
500.	Economiser & Cover.	--	Brick. Corrugated iron.		12811.0	730	.	.	1	$1\frac{3}{4}$									
501.	Shaft.	--	Brick.		13794.0	1076	.	.	1	$6\frac{3}{4}$									
502.	Box & Tray Store.	1892	Corrugated iron. Roof, slates & zinc. Floor, boards.		23607.0	E 295	.	.	3										
503.		1894	Brick & Wood. Roof, Millersden paper. Floor, boards.		4622.0	E 58	.	.	3										
504.	Packing House. Traverse.	1892	Brick. Roof, zinc covered. Floor, Asphalté. Earth, with concrete retaining wall.		13531.0	445	.	.	8										

M. 319.  
no trace

M. 320. no trace

M. 349 ✓

N. 579 ✓

No.	Description	When built	Construction	Dimensions	Cubic Contents	Cost of Buildings where known			Price per cubic foot			Depreciation			Valuation			Remarks	No.
						£	s	d	£	s	d	£	s	d	£	s	d		
505.	Store.	1892	Wood. Roof, felt covered. Floor, concrete.		8806.0	E	147	.	.	4									
506.	Mud Washing Shed. Traverse.	1891	Wood & brick. Roof, felt covered. Floor, lead covered. Earth.		891.0	E	19	.	.	5									
507.	Wash Water Jetting House.	-	Wood. Roof, zinc covered. Floor, lead covered & boards.		9787.0	E	204	.	.	5							N. 574. ✓		
508.	Office (Principal Foreman (white))	1894	Wood, matchlined throughout. Roof, felt covered. Floor, boards, & lead covered.		6794.0	E	141	.	.	5							N. 576. ✓		
509.	Experimental House.	1892	Wood & brick. Roof, felt covered. Floor, boards		5885.0	E	123	.	.	5							N. 573. h/m		
510.	Acetone Store.	-	Brick. Roof, slates. Floor, concrete.		41544.0	E	865	.	.	5							N. <del>570.</del> 569		
511. 515.	Acetone Store.	1891	Brick. Roof, slates. Floor, concrete.		52964.0	E	1104	.	.	5							N. 571. h/m N. 567.		

No.	Description.	When built.	Construction.	Dimensions.	Cubic Contents	Cost of Buildings where known.			Price per Cubic foot	Depreciation.			Valuation.			Remarks.	No.
						£	s	d.		£	s	d.	£	s	d.		
512, 516.	Box House.	1891	Brick. Roof, slates. Floor, Asphalté.		52,964.0	£	1104.		5							N. 572. N. 568.	
513.	Hydrant Hose Ho.	1895	Wood. Roof, felt. Floor, Concrete.		14,96.0	£	25.		4								
514.	Acetone Store.	1893	Brick. Roof, slates. Floor, Concrete.		82,144.0	£	1711.		5							N. 566.	
517.	Sorting House. * Cylinder Cutting Ho.	1891	Brick. Roof, slates. Floor, Concrete.		69,892.0	£	1435.		5							N. 562. N. 563.	
518.	Condite Tray Store. Porch.	1894	Brick, Zinc lined throughout. Roof, slates. Floor, lead covered. Wood. Roof, slates.		9210.0	£	230.		6							N. 557.	
519.	Police Hut.	1892	Wood, matchlined. Roof, felt. Floor, boards.		1170.0	£	29.		6							N. 556.	







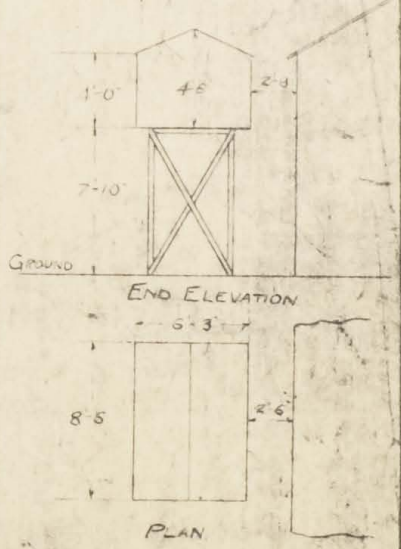
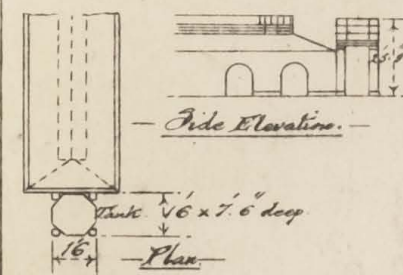
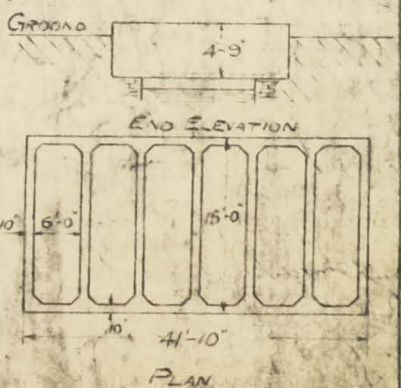
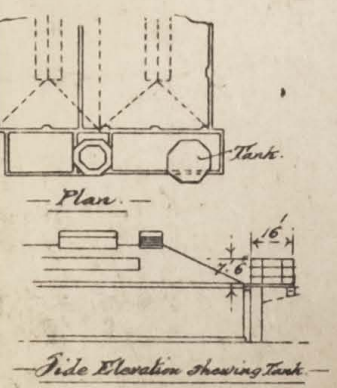






No.	Description.	When built.	Construction.	Dimensions.	Cubic Contents	Cost of Buildings where known.			Price per cubic foot.			Depreciation.			Valuation.			Remarks.	No.
						£	s	d	£	s	d	£	s	d	£	s	d		
563	Magazine. Shoe Trench. Traverse	1903-4	Brick. Roof, Copper covered. Floor, Asphaltic. Floor, boards. Earth.		30,188.0	1439	.	.	11½								P. 714		
564	Magazine. Shoe Trench. Traverse.	1903-4	Brick. Roof, Copper covered. Floor, Asphaltic. Floor, boards. Earth.		30,188.0	1439	.	.	11½								P. 716		
571	Acetone Recovery Plant. Water Tanks (10,000 gallons) & Girders.	1905-B	Brick & Corrugated Iron. Roof, Slates & glass. Floor, Concrete & blue brick. Iron throughout		163,774.0	2,953	.	.	4¼								RS 639		
572, 584	Hydrant Hose Ho.	1905	Wood. Roof, Slates. Floor, Boards.		2,184.0	55	.	.	6								RF. 563		



Map No.	Description	Construction	Dimensions	Cost of Buildings where known \$ & d	Map No.	Description	Construction	Dimensions	Cost of Buildings where known \$ & d
64-478 N.L. N. 504	Water Tower Water Tank (10,000 gallons)	Iron throughout.		Included in Cost of Building.	433 6444	Boiler & Pump House Water Tank (10,000 gallons) & Girders.	Iron throughout.	 Section.  Side Elevation.	120
184 6149	Incorpor. Ho. Group E. Water Tank (8,000 gall)	Iron throughout.		80	571 R5659	Acetone Recov. Plant Water Tank (10,000 gallons) & Girders.	Iron throughout.		110
282	Refining House Water Tanks (2) 5000 gall	Iron throughout.		90	83c 830	Water Tank (300 gallons) See 83a).	Tank Galvanised Iron Covered in with boarding 6 x 1 & packed all round with asbestos Supported on Wood girders 6 x 4 & 4 x 3"		
422 6417	Vat House Water Tanks (10,000 gallons) & piers.	Iron throughout. Brick.		120	78f 78	Oil Tanks	Tanks Reinforced P.C. Concrete Supported on Piers to ballast		
429 6417	Nitrating House Water Tank (10,000 gallons) & Girders.	Iron throughout.		130					

Map No	Description	When Built	Construction	Dimensions	Cubic Contents	Cost of Building where known	Price per Cubic Foot	Depreciation	Valuation	Remarks	No
2a	Wet Guncotton Magazine	1915	Roof - Asbestos-cement tiles on boarding, timber trusses Walls - Asbestos-cement sheets on timber framing, (external) Dwarf walls in brick Floor - 4" Concrete. Foundations - Concrete (reinforced) Timber Piles at intervals.		37,275 - 0	£ 410	£ 2 3/4			Note - Buildings Marked D Built by Director of Barrack Construction the cost of which is not separately recorded are calculated to have cost on average price of 7 1/2 per cub ft.	
3a	E.C.		Timber (boards) throughout.		124 - 6						
16a	Guncotton Store	1916	Timber framed, matchlined Roof - 3-bly ruberoid on bding Floor - Concrete, lead covered. Foundations - Concrete to ballast. Earth traverse, brick retaining wall.		Building 11385 - 0 Traverse 14605	D 200	7 1/2				
17a	Engine and Fan House	1916	Timber Framed, Roof - Ruberoid on boarding Floors - Concrete Foundations - Brick and Concrete.		3306 - 6	D 150	7 1/2				
18a	Guncotton Store	1916	See 16a.	See 16a	11745 - 0	D 200	7 1/2				
<del>22a</del>	<del>do</del>	<del>1916</del>	<del>do</del>	<del>do</del>	<del>11385 - 0</del>	<del>D 200</del>	<del>7 1/2</del>			<del>Demolished.</del>	
22a	QUINAN STOVE	1916	See 17a	See 17a	3506 - 6	9 1/2	7 1/2				
22b	ENGINE RM for above.										
28a	Engine and Fan House										
28b	E.C.	1918	Roof - 2ok on boarding Walls - Weatherboarding on timber framing Floor - Concrete slab.		464 - 0	6 1/2					
33A	PUMP HOUSE										
<del>36a</del>	<del>E.C.</del>	<del>1916</del>	<del>4 1/2 Brick, Concrete slab, 56' x 100'</del>	<del></del>	<del>291 - 0</del>	<del>6</del>				<del>Demolished</del>	
36a	Engine House										
36b	C.E. Crude Clearing House.	1917	Roof - 2ok on boarding Walls weatherboarding on timber studding, match-lined inside and under collars. Boarded floor.		436 - 9	6 1/2	7 1/2				





Map No.	Description	When Built	Construction	Dimensions	Cubic Contents	Cost of Building where known			Price per Cubic Foot			Depreciation	Valuation	Remarks	No
						£	s	d	£	s	d				
<del>37n</del> 37o ✓37 <sup>9</sup>	<del>Drowning Shed</del> Filter House } Annex	1916	<del>Timber throughout.</del> Roof: - Lok. Floor: - Ashes. 37o, weather boarded and louvered on three sides 37n, roof only, with louvered vent: 20' x 6' x 20'		14500'	128	-	-	63						
37p	Waste Acid Settling House (No 1)	1917	Roof: Corrugated Iron. Timber Trusses Timber posts. Sides louvered 3'5" from eaves, rest open Floor: Blue brick on concrete.		7177'										
✓37q	Drum Oven	1917	Roof: - Lok on boards. Walls: - 7/2 Brick (Stocks) Floor: Concrete.		386'	35			10						
<del>37r</del>	<del>Piers for Absorption Towers.</del>	1916	<del>Concrete, blue brick facings Concrete slab and piles</del>		185'										
<del>37s</del>	<del>do</del>	1916	<del>As 37r. Arched portion, of Piers with blue brick facings.</del>		557'										
38a	N.G. Office - now laboratory	1908	Roof: Slates on boarding. 9" Brick walls, rough-cast externally, plastered internally. Floor: - Boards on joists. Concrete slab, founds, and piers to ballast.		8997'	180			48						
38b 386	Hose and Smoke- Helm House.	1917	Roof: Lok on boards. Sides: Weather boarding on timber. Floor: Concrete.		874'	130									
38c 38c	Wheel-stretcher House	1918	Lok on timber, sides and roof. Floor: - Ashes.		173'	6	15			0.4					








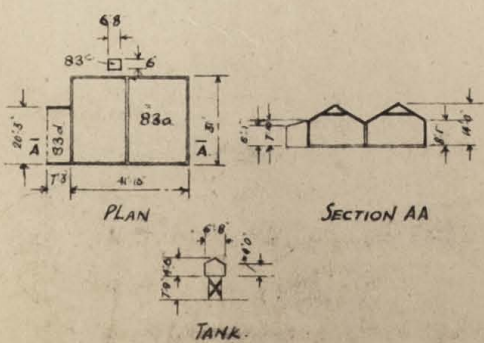
Map No	Description	When Built	Construction	Dimensions	Cubic Contents	Cost of Building where known			Price per Cubic Foot			Depreciation	Valuation	Remarks	No
						£	s	d	£	s	d				
39 <i>39</i>	C.E. Grade 1A Purification House	1918	Corrugated Iron (Roof and sides) on steel-framing. Floor: Blue Bricks on Concrete. Foundations: Concrete, piled. Interior platform timber decked.		40833'	1885	-	-	11						
<del>39a</del>	<del>Absorption Towers</del>	<del>1918</del>	<del>Fleltions with blue-brick facings. Concrete piers to ballast.</del>	<del></del>	<del>140 + 336</del>	<del>11</del>									
<del>39c</del>	<del>C.E. Grade 1A Purification Plant (Temp)</del>	<del>1918</del>		<del></del>	<del>5227'</del>	<del>358</del>			<del>1 4 1/2</del>						
<i>39c</i>	<i>M/c Shop</i>														
<i>39b</i>	<i>?</i>														
<i>39d</i>	<i>STORE</i>														
<i>48a</i>	Foremens Dining and Shifting Room	1916	Roof - Ruberoid. Weatherboarding on timber. B.C. matchlined interior. Floor (a) Concrete (b/c) Boards.		2362'	41			4.15						
<i>39E</i>	<i>Electrician Shop</i>														
<i>48b</i>	Cycle Shed	1917	Roof Rok, Timber framed. Floor, Ashes. Racks for 19 cycles.		946'	n									
<i>47a</i>	<i>Air Reservoir Tanks</i>														
<i>47b</i>															
<i>53a</i>	N.G. Weighing House	1915	Timber framed, weather-boarded exterior, matchlined interior. Roof: Ruberoid. Floor: lead-covered on concrete. Foundations: Concrete. Earth traverse, brick retaining wall.		11,996'	D.									
<i>53b</i>	<i>Refrigerator House</i>														
<i>48c</i>															
53b	Loading Stage	1915	Corrugated Iron on Timber framing, Floor: part boarded.		925'	D.									

*Original building demolished and rebuilt 1941.*



Map No	Description	When Built	Construction	Dimensions	Cubic Contents	Cost of Building where known			Price per Cubic Foot			Depreciation	Valuation	Remarks	No	
						£	s	d	£	s	d					
<del>68b</del>	<del>Demerating Plant</del>	<del>1917</del>	<del>Timber framed throughout open-sided, + ends. Rok Roofing Floor Ashes.</del>	<del></del>	<del>7230</del>	<del>92</del>	<del>-</del>	<del>-</del>	<del>3</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>demolished.</del>
<del>68c</del>	<del>Detetrylating Plant</del>	<del>1917</del>	<del>Timber framed throughout Sides, above first floor weatherboarded, below, open. Louvered, 2'6\"/&gt;</del>	<del></del>	<del>4605</del>	<del>27</del>	<del>-</del>	<del>-</del>	<del>585</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>demolished.</del>
<del>68d</del>	<del>Detetrylating Plant</del>	<del>1917</del>	<del>Corrugated Iron on Timber open-sided except for portion of one side. Brick reorts and chimneys</del>	<del></del>	<del>9077</del>	<del>47</del>	<del>-</del>	<del>-</del>	<del>1 1/2</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>demolished</del>
<del>71a</del>	<del>Mixed Acid Tanks</del>	<del>1916</del>	<del>Steel on brick (blue) Sleeper walls.</del>	<del></del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>demolished</del>
<del>71b</del>	<del>Cover for Nitre Cake Pans.</del>	<del>1917</del>	<del>Roof: Tiles on battens. Timber throughout. Open sided</del>	<del></del>	<del>6417</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>See 72c</del>
<del>72a</del>	<del>N.A. Factory No.1.</del>	<del>1916</del>	<del>Roof: Rok on boards. Sides and Gables: Corrugated Sheeting on Steel framing, Steel Platforms. Retorts: brickwork Floor: Blue paviers on Concrete Founds: Concrete piled.</del>	<del></del>	<del>Super-Structure 228,046 Foundations 8,100</del>	<del>2530</del>	<del>-</del>	<del>-</del>	<del>255</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>demolished</del>
<del>72c</del>	<del>Cover for N.C. Pans.</del>	<del>1917</del>	<del>Pantiles on battens. Steel stanchions and roof qunders. Floor: Ashes.</del>	<del></del>	<del>Super-Structure only 13,500 6,417 2,180 11,530 33607</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>demolished</del>
<del>72b</del>	<del>Nitric Acid Factory No.2.</del>	<del>1917</del>	<del>Construction as 72a. Roof: Pantiles on battens.</del>	<del>See 72a.</del>	<del>236,196</del>	<del>2922</del>	<del>-</del>	<del>-</del>	<del>3</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>demolished</del>
<del>72d</del>	<del>Cover for N.C. Pans.</del>	<del>1917</del>	<del>Construction as 72c. Five bays, only.</del>	<del>See 72c. Length 62'0\"/&gt;</del>	<del>11,160 33607 44767</del>	<del>457</del>	<del>-</del>	<del>-</del>	<del>2.45</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>-</del>	<del>demolished</del>



Map No.	Description.	When Built	Construction	Dimensions	Cubic Contents	Cost of Building where known			Price per Cubic Foot			Depreciation	Valuation	Remarks	Yo	
						I	S	D	I	S	D					
<del>72e</del>	<del>Acid Collectors</del>		<del>5 Tanks on Concrete and Blue brick base</del>													
72g	Acid Absorption Towers	1917	Concrete, with blue brick facings, on concrete slab paved with blue bricks Piles to ballast		1134											dem.
72h	do	1917	As 72g		1172 foundations 280											dem.
73a	E.C	1916	Roof: Slates on boarding Walls: 4 1/2 brick Floor: Concrete		107											
74a	G.C. Stove No. 18	1916	Construction as 16a.	See 16a.	381											74A GC Stove demolished by explosion & rebuilt on same
75a	Motor House	1916	Roof: Ruberoid on boarding Timber framed, weatherboarded exterior Floor: Concrete.		1880	60										dem. Rebuilt adj. Bldg 74a.
76a	G.C. Store No. 19	1916	Construction as 16a.	See 16a.	381											
76b	loading Stage.		Roof: Ruberoid on boarding Timber & boarding (FE) Floor: Part Boarded, part tarmac.		621	20										
80a	Boiler House No. 2.	1917	Corrugated iron, self supported roof and sides Sides partially open 5' from ground. Timber framing, Concrete floor. Boiler with 60' steel shaft		9477	17					1.2					Demolished
83a	Shifting Room.	1916	Roof: Ruberoid on bding Timber framed, weatherboarded exterior, match-lined interior. Floor, Concrete Brick Dwarf walls on concrete founds. Centre timber partition. Cycle Shed, asphalt floor. Water tank on trestle boarded in		15,349 Tank: 480	202					5 1/2					demolished

73a ✓

74a ✓

75a ✓ Motor House

76a ✓



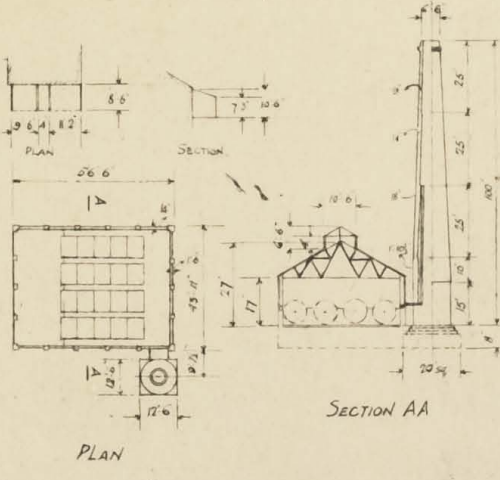
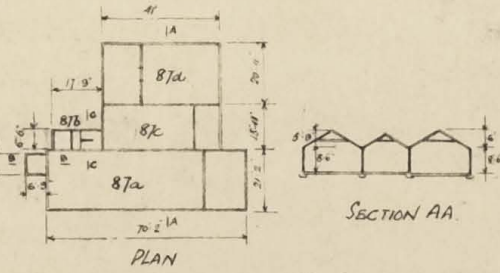

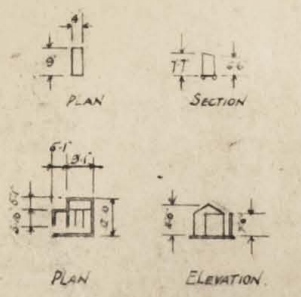
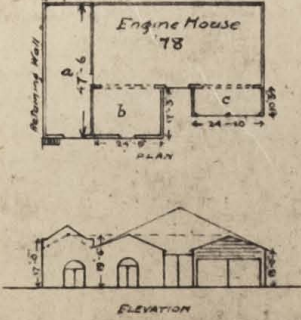
76b ✓ loading Stage. No. 91 d. Change Ho.

79a ✓ Dem. 80a ✓ New Boiler

83a ✓ (See 83c)

84a ✓ Cycle Shed

No. 099.

Map No	Description	When Built	Construction	Dimensions	Cubic Contents	Cost of Building when known			Price per cubic foot			Depreciation	Valuation	Remarks	No	
						£	s	d	£	s	d					
<del>83b</del>	<del>Matron's Room</del>	1915	Timber throughout. Matchlined interior, weather boarded exterior. Floor boarded, roof covered "Lok".		1283'											
83c	See Sheet 66a. Water Tank															
85d	Bicycle Shed	1914	Roof "Lok" on boarding. Ends weatherboarded. Earth floor.		1887'											
86a	Boiler House No. 3	1916	Roof Slates on boarding. Steel Trusses Loured and glazed vent full length. Walls: Brick 14 Panel, 18 Piers. Floor: Concrete. Foundations Concrete to Ballast.		78003'	2737										
86b	Chimney Shaft															
87a	N.G. Shafting Room	1916	Timber framed, "Lok" roof covering. Weatherboarded exterior. Floors, concrete.		18767'	237										
87b	E.C. and Lavatory	1918			936'											
87c	Women's Dining Room				8200'	203										
87d	Mens do.				10,762'	187										
87e	E.C.	1917	Timber framed, "Lok" roof weather boarded exterior, Floor, Concrete.		252'											
87f	E.C.	1916	Brick, Slated Roof, Concrete Floor.		1380'											
87g	EC Women															
78 (a, b, c)	Engine House (Additions to)	1916	Brick built. Slated Roof boarded inside. Wood trusses to a & c & iron burlins to b. Floor concrete broken by plant & stanchions. Front of c consists of double doors & weather boarded gable.		a 13250' b 6940' c 4135'	2158										
78d	See Sheet 100															
78e	- do															
78f	See Sheet 66a															

*demolished*

*87 - 1916*

*87a 87c 87d 87e 87f 87g*







*87e 87f*

*87g EC Women*

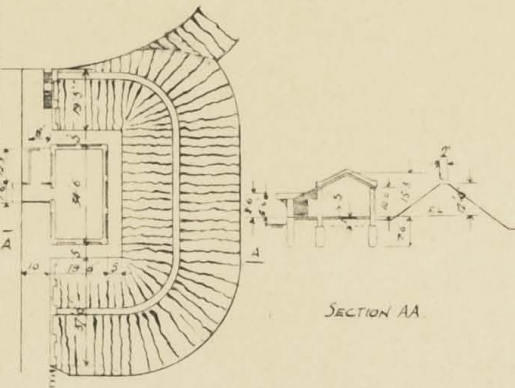

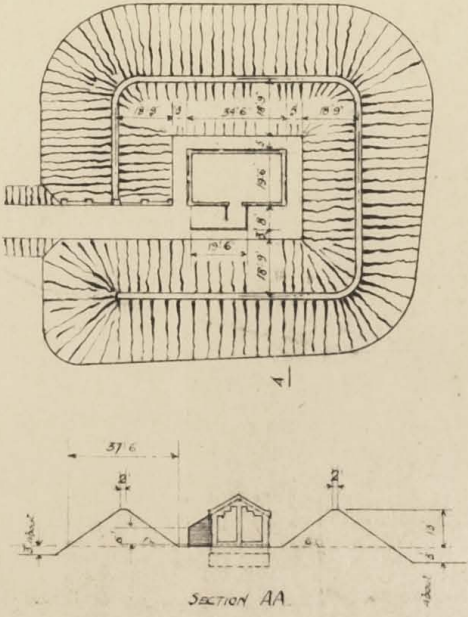


*78 (a, b, c) 78d 78e*

*78e - do*

*78f See Sheet 66a*

Map No	Description	When Built	Construction	Dimensions	Cubic Contents	Cost of Building where known			Price per Cubic foot			Depreciation	Valuation	Remarks	No
						L	S	D	L	S	D				
<del>88b</del>	<del>C.E. Store</del>		<del>Timber throughout. Roof covered canvas.</del>	<del></del>	<del>525'</del>									<del>Demolished.</del>	
<del>89a</del>	<del>E.C.</del>	<del>1917</del>	<del>Timber throughout. Exterior weather boarded. Roof: "Rok".</del>	<del></del>										<del>Demolished.</del>	
<del>93a</del> 94a ✓	Still House.	1915.	"Rok" Roofing, Timber Trusses, walls, timber framed, weather boarded exterior, matchlined interior. Floor, Concrete.		7384'	138				4 1/2					
<del>95a</del>	<del>C.E. Purification Plant</del>	<del>1915.</del>												<del>Demolished.</del>	
95b ✓	How. House.														
95c 95e	C.E. Clearing House No. 1.	1915.	Timber framed, weather- boarded exterior, "Rok" roof. Floor, Concrete, asphalt covered. Interior compart- ments of wrot. boards.		2481'	75				7 1/4					
95d ✓	C.E. Clearing House No. 2.	1915	As 95c	As 95c.	2481'	82				7.9					
96a ✓	C.E. Store No. 2.	1916	Construction as 16a	See 16a	D	351'									
96b ✓	C.E. Store No. 3.	1916	Construction as 16a	See 16a	D	211'									
98a ✓	G.C. Stove No. 22	1916	Construction as 16a	See 16a.	12,223	850				1.47					
100a 100g ✓	E.C.	1918.	Roof: "Rok" on boarding. Walls: 4 1/2 flettons. Floor: Concrete.												
104a ✓	C.E. Stuffing Room.	1916.	Timber framed, weather-boarded exterior, "Rok" roof. Floor: Concrete Central partition, matchlined os. Tank on trestles, boarded in.		10,969'	211.				4 1/2					



Map No	Description	When Built	Construction	Dimensions	Cubic Contents	Cost of Building where known			Price per Cubic foot			Depreciation	Valuation	Remarks	No	
						L	S	D	L	S	D					
105a <i>105a</i>	Paste Store No. 4.	1916	Building and Porch as 88a.		10057	3	0	0							✓ L. 101. ✓	
108a <i>108a</i>	E.C.	1918	4 1/2" Brick (Flettons), Roof: Asbestos Corr <sup>d</sup> Sheets: Floor: Concrete.		289	0	11	0	0							
111a	Paste Store No 5	1916	Building and porch as 88a.		10057	0										
123a	Loading Stage	1917	Timber, weatherboarded outside, Roof: Gal. Floor, Part concrete asphalt covered.		856	0	11	0	0							
123b	E.C. See Sheet 88															
128a	Pump House and Well.	1916	Roof: "Ruberoïd" on boarding hipped. Walls: Brick 9" Floor + Foundations: Concrete. Covered well in brickwork.		545	0	11	0	0							

✓ L. 101. ✓

L. 131. ✓

L. 132. ✓

Map No	Description	When Built	Construction	Dimensions	Cubic Contents	Cost of Building where known	Price per Cubic foot	Depreciation	Valuation	Remarks	No
128b 129a	E.C. Press Ho. No. 2.	1917 1916	129a. Roof: Ruberoid on boards, steel trusses and stanchions. Walls: Brick 18. Partition Walls to 1'6" above roof. Timber partitions facing verandah. Floor: concrete, asphalt covered. Founds: Concrete. Truck Porches, Ends, Timber weather-boarded outside. Roofs covered Ruberoid; Tipped; Side, Galv <sup>d</sup> Cor <sup>d</sup> Iron on timber (sides & roof). 128a. Roof: "Rok" on boards. Timber, weatherboarded outside. Floor: Boards.		1433'	£    s    d D.    0    0 £    0    0	£    s    d			L. 134. ✓  L. 117. ✓	
132a	Wash House.		Wooden Cupboard on 4 legs		53'	D				L. 137. ✓	
134	Press House No 3 One bay extension	1912	Roof: Zinc on boards, steel truss and stanchions. Walls: Brick 18. Floor: Concrete asphalt covered. Founds: concrete 4' Matchlined dado round walls, Truck porch removed and refixed.		8645'	D £    s    d					
134a	E.C. and extension to truck porch N. end No. 3 Press House	1917	E.C. Timber weatherboarded exterior, Roof Rok Floor, Concrete. Porch. Galv <sup>d</sup> Cor <sup>d</sup> Iron on timber studding.		325' 6"						
143a	Incorporating House No. 1.	1916	Roof: Ruberoid on boards. Walls: 18" Brick, projecting 1'6" above roof 9" thick. Removeable sides to each compartment in steelwork with timber panels. Verandah Stanchions in steel. Floor: Concrete reinf <sup>d</sup> R.S.s asphalt covered. Founds: Concrete							L. 143. ✓	
144 <sup>a</sup>	Heat Test Room					£    s    d 1000    0    0 200    0    0				L. 119. ✓	


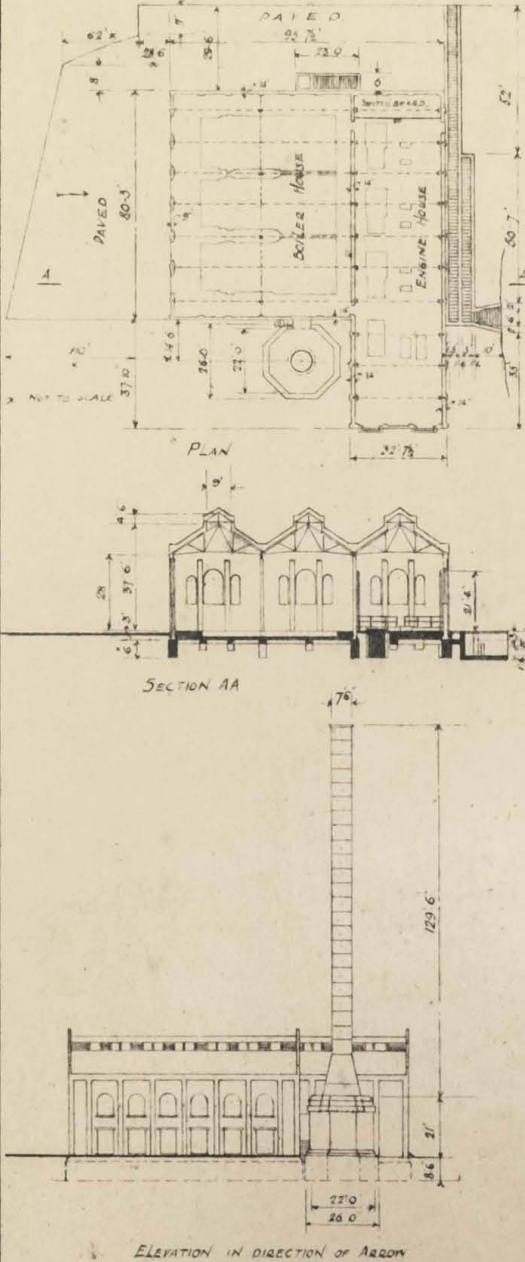

Map No	Description	When Built	Construction	Dimensions	Cubic Contents	Cost of Building where known	Price per Cubic foot	Depreciation	Valuation	Remarks	No.
144b	Silvered Vessel House	1912	Timber, covered urabite inside and outside		1000'	35				L. 120 ✓ L. 123. NT	
144c	Silvered Vessel House	1914	Construction as 144b.		1000'	55	18.4			L. 128. ✓	
150a	Fuse Powder Magazine No 2	1915	Roof: Asbestos corr sheets (Corrament) on battens. Walls: 14 brick, matchlined interior throughout, and under eollars, carried on 2.C. beams Floor: timber, covered Corticine Founds: Concrete and R.C Piles		13,142'	517	9 1/2			LF 147. ✓	
151a	E.C.	1917	Roof: Corr <sup>a</sup> Asbestos on timber purlins brick walls concrete floor.		675'					L. 146. ✓	
152a	Incorporating House No. 2	1916	Roof: Ruberoid on boards Walls: 18 brick, projecting 1'6" above roof + 9" thick Removeable sides to each compartment with timber panels Verandah Stanchions in steel Floor: Concrete reinf <sup>d</sup> with R.S.I.s, asphalt covered Founds: Concrete		46,977'	1800				L. 151 ✓ L. 155 ✓	
156a	E.C. As 163a										
161a	Incorporating House No. 7. A	1916	Construction and dimensions as 152a								
162a	Incorporating House No. 5.	1916	do.								
	Traverse	1916	Concrete throughout.								
162b	EC. See Sheet 88.			Approx <sup>d</sup> Length on 1/4 at base = 643'							
163a	E.C.	1917	Roof Asbestos Corr <sup>a</sup> Sheeting on timber: Walls: 4 1/2 Brick, f'ettons Floor: Concrete.		782'						


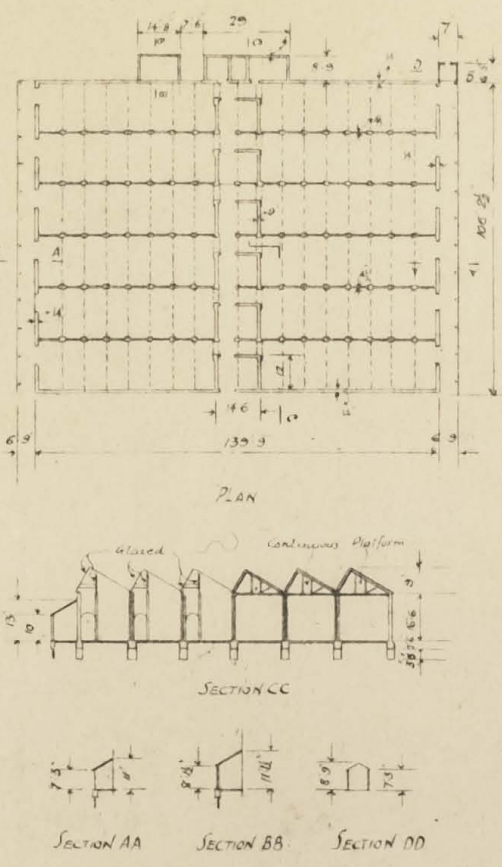







Map No	Description	When Built	Construction	Dimensions	Cubic Contents	Cost of Building where known			Price per Cubic Foot			Depreciation	Valuation	Remarks	No.
						£	s.	d.	£	s.	d.				
174a	Shed for Tar Boilers.		Corr. Iron Roof on framework sides partly cov <sup>d</sup> in. Earth floor		1253	£	s.	d.	£	s.	d.				
190A	Mineral Jelly Store No. 2.	1916	Roof: on boarding. Timber Trusses. Brick walls, 9" and 14". Floor, Concrete. Foundations: Concrete Platform, interior, wood and steel. Ovens, interior, Brick and R.C. W.I. grids Charging Platform. Roof on bas. Floor, boards on brick wall.		13433	501	-	-	-	0					
192a	Hose House	1915	Roof: Lok on boards. Timber framed, weather boarded outside. Floor, Concrete.		720	2								LF. 171	✓
209a	Pump and Accumulator House	1915	Pump House. Roof: Slates on boarding, steel trusses. 14" Brickwork, with 9" panels. Floor: Concrete. Foundations: Concrete, piers to ballast. Accumulator House. Timber roof, covered slates, hipped. Walls: panelled brickwork, varying from 2'7 1/2" at bottom to 9" at top. Foundations: Mass Concrete to ballast. Covered well in 9" brickwork.		21694	876				9 3/4				AE 214	✓
209b	Oil Condensing Tanks, etc	1917, 1918	Tank 2. Concrete, internal walls, brickwork 9", rendered in cement mortar. Foundations: Concrete piers to ballast. Well: 9" brickwork, rendered open at top. W.I. Handrail. Condenser tanks: Concrete slab 10-23', with concrete piers to ballast, 9" brick walls under tanks 2'7" high.		143									AE 213	NT

No foundation measured.

Map No.	Description	When Built	Construction	Dimensions	Cubic Contents	Cost of Building where known			Price per Cubic Foot			Depreciation	Valuation	Remarks	No.
						L	s	d	L	s	d				
211a	Matrons Room	1915	Roof: Lak on boards Timber framed, weather-boarded outside, match-lined inside. Floor-Boards.		4701	136	-	-	-	-	7				
213a	Power House	1917	Roof: Slates on boarding Steel roof trusses on steel stans. built in walls. Hand crane carried on R.S.J gandy in Engine House. Walls: brick Founds: Concrete Culverts in concrete boarded in Ventilators alternately loured and glazed glazed top full length Steel chimney on concrete foundation Area paved in concrete		37362'	1200	0	0						AE 210. ✓	
232a	Engine House	1916	Roof: Slates on boarding Timber Collared rafters. Walls: 9" Fletton Bricks. Floor & founds: Concrete (R.C.) Sliding Doors, R.C. Lun'ol over Inspection Pit, 19'-0" long x 4'3" x 2'6" deep, Concrete (reim. d)		7175'	248	-	-	-	-	8.3			HE. 13. ✓	

Map No.	Description	When Built	Construction	Dimensions	Cubic Contents	Cost of Building where known			Price per Cubic Foot			Depreciation	Valuation	Remarks	No.
						L	s	d	L	s	d				
245a	Ticket Station	1915	Roof: Ruberoid on boarding Timber throughout Floor: Asphalt Paved.		1404	L	s	d	L	s	d			No foundations measured <b>A. 235 + A 236.</b>	
246a	Press Ho. No. 10	1916	Roof: Oak on boarding Timber N-light trusses, glazed one side. Walls: Exterior, Yellow Sticks, Interior, Plasters, painted Floor: Concrete, asphalt covered, reinf. Founds: R.C. Concrete, Concrete piers to ballast Shoe: Porch, Timber, weather boarded outside, Wood Floor on concrete (DD).		406213	8700			5					<b>H. 16.</b> ✓	
249a	Timber Store	1911	Roof: Corrug <sup>d</sup> Iron, Timber trusses, open sided. C.I. Columns. Racks in timber. Founds: Concrete blocks. Floor: Earth.		3860									<b>AB 244</b> ✓	
249c	Petrol Store See Sheet 88													<b>AB 251</b> ✓	
250a	Store	1915	Roof: Oak on boarding Timber rafters with collars. Walls: Timber framed, matchlined interior to eaves, weather boarded ext. Floor: Boards. Founds: Timber blocks.		16030	160			2	4				<b>A.B. 245</b> ✓	
245b	Office and Dining Room	1918	Brick: Plasters 4 1/2 and 9' thick. Roof: Timber covered Oak. Floor, concrete. Loured vent <sup>l</sup> : 8' and 5' long. Shed: in timber weather-boarded, Oak roof, Floor, boards.		6242	176			6	3	4				






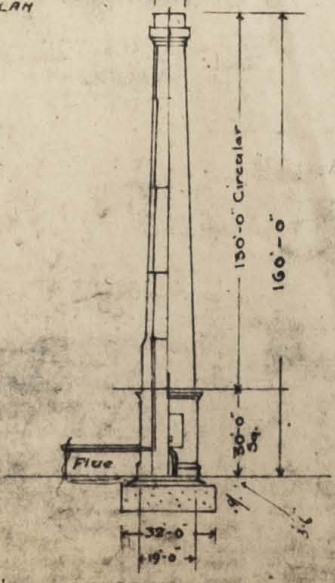
Map No.	Description	When Built	Construction	Dimensions	Cubic Contents	Cost of Building where known			Price per Cubic Foot			Depreciation	Valuation	Remarks	No
						L	s	d	L	s	d				
259a	Hose House	1916	Roof: Lok on boarding Timber framed weather-boarded outside Floor Concrete		1050'									HF 20	NT
260a	Stoke Hole	1916	Roof: Lok on boarding Brick walls Floor Concrete		3488									H. 17	NT
261a	Womens Dining and Shifting Room	1916	Timber buildings, weatherboarded outside, matchlined inside to eaves. Roofs timber cored. Lok. Floors, boarded on timber joists, carried on brick sleeper walls and concrete founds Floor to Kitchen and E.Gs. concrete		201673	6167	-	-	735					H. 19	Hip roof
260b	Boot Changing Room	1917	Boat-changing and drying rooms 4 1/2 Brick walls, flutings, with piers at externals. Timber roofs, cored Asbestos Corr <sup>d</sup> Sheeting Floors. Concrete.		22401	332	-	-	4 1/4					H. 18	?
					224074	6569	-	-	7						

Map No.	Description.	When Built.	Construction.	Dimensions	Cubic Contents	Cost of Building where known			Price per Cubic Foot.			Depreciation	Valuation	Remarks	No
						£	s	d	£	s	d				
272a	Worktakers' Office and Bicycle Shed.	1918	Brick (9" Flettons) Building Concrete Floor, Timber roof, covered "Lok".		5066'	209			8-3					H 23. ✓	
273a	Pump House and Sewage Tanks.	1916	Pump House, Timber framed, weather boarded outside, roof covered Lok Tank in Concrete reinf.			20								HE 24. ✓	
275a	Wood, coal and Cycle shed.	1917	4 1/2" Brick (Flettons) with 9" piers. Timber roof covered Lok Floor: Concrete.		1250'	66			1 0 3/4						
275b	Womens Hospital.	1917	Timber building Roof: Covered Lok; walls, weather boarded exterior, lined Asbestos flat sheets interior. Chimney Stacks in brick. Floors, boarded on timber joists. Verandah floor concrete. Foundations, brick sleeper walls on concrete.		45,170'	2264			1 0						
279.	Extension to Crystallizing House, Salt petre Refinery	1917	Walls: brick, outside facing yellow stock (reused), interior flettons (new). Roof timber covered old tiles on battens Floors, boarded on timber joists. Interior framework in steelwork, supporting floors, and tank (41.8'-8'-8') on roof. South wall supported on steelwork. Ground floor, concrete. Foundations: Concrete beams, and piers to ballast. Lead covered flat under tank.		55335	2687			11-2					A 279. NT	
														No foundations measured.	



Map No.	Description	When Built	Construction	Dimensions	Cubic Contents	Cost of Building where known			Price per Cubic Foot			Depreciation	Valuation	Remarks	No.
						£	s	d	£	s	d				
269a	Cycle Shed Main Gate	1916	Timber framed three sides, weatherboarded exterior. Roof Lak on bding Floor, earth. Timber racks for 70 bicycles.		3516	110								A. 227. ✓	
do.	do.	1916	As last, racks for bicycles.		1680									Demolished	
do.	do.	1916	Timber ends weather-boarded open sides with posts carrying timber roof, covered Lak, Floor, Earth racks for 100 bicycles.		5720									Demolished	
249c	Petrol Store	1917	Brick: 4 1/2 and 9 Flettons. Roof: Timber covered Lak Floor: Concrete		570	24	10	-			10.3			A.B. 251. ✓	
162b	E.C.	1917	Brick, 9 Flettons. Roof: Lak on timber. Floor: Concrete. Corrugated Iron Screen, front.		977										
131a	E.C.	1917	Brick walls, Roof, timber covered slates, Floor, Concrete.		750									L. 117. ✓	
123b	F.C.		4 1/2 brick walls. Timber rafters boarded + slates timber partitions. inside Floor. Concrete.		1348									L. 131.	

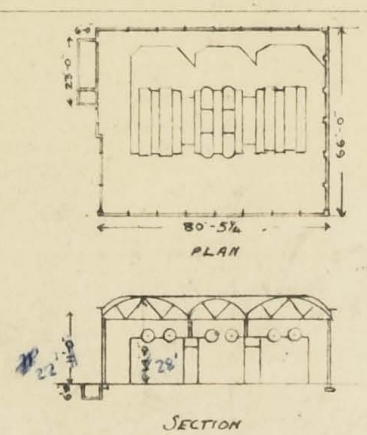





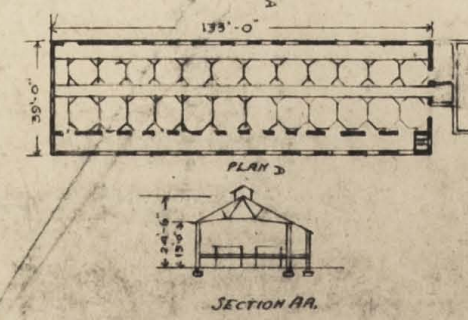
No foundations measured.









Map No	Description	When Built	Construction	Dimensions	Cubic Contents	Cost of Building where known			Price per cubic foot			Depreciation	Valuation	Remarks	No.		
						£	s	d	£	s	d						
376 <sup>a</sup>	Ether Tanks	1918	Two Circular Tanks														
376 <sup>b</sup>	Do.		23 feet dia. & 22.6 high Cast iron Section plates bolted and rusted jointed standing on cross Girders carried on 18" Steel Stools on Circular Concrete foundations.		9348'												
399 <sup>a</sup>	Magazine	1915	Brick walls. Concrete foundations on piles. Studded & weather boarded walls. Floor joists & boards leather covered. Roof boarded, covered Rok felt.		613'												
399 <sup>b</sup>	Gunpowder Pellet House.	1915	Concrete foundations on piles - Studded and weathered boarded walls. Floor joists and boards. Roof boarded & Rok felt.		5556'	273				11 1/2							
405 <sup>a</sup>	Pump House.	1915	Concrete foundations on piles. Brick walls. Floor part 2x deals. part concrete - Roof boarded and slated.		6528'	447.				1 4 1/2							
405 <sup>b</sup>	Dry Gun cotton Yarn Store.	1918	Timber framed sidss covered with Ruberoid lined with Uralite & Painted calico over joists, Roof covered Ruberoid, Floor covered lead Fan House Extension 9' brick walls. Roof covered Ruberoid, Floors concrete covered lead.		10.025	636				1 4							
405 <sup>c</sup>	Chimney.	1917	1 1/2 stock brickwork. Circular on plan with concrete cap 130 ft. high & standing on 19 ft. square pedestal 30 ft. high Total height 160 feet.		40946'	2235	-	-		1 0							

MF. 317. ✓

GE 400 ✓



Map No	Description	When Built	Construction	Dimensions	Cubic Contents	Cost of Building where known			Price per Cubic Foot			Depreciation	Valuation	Remarks	No	
						L	S	d	L	S	d					
405 d	Boiler House N.C.	1916 + 1918	Walls 27x18 brick piers with 4x brick panels Roof Semi-circular black corrugated sheets on steel principals resting on steel joists. Floor Concrete Foundations 3'0 deep.		74,382 ft.	1400			4 1/2				GE 400 ✓	No foundations measured.		
408 a	Guard House	1915	Walls - Studded and weathered boarded Roof Boarded + Felt. Floor boarded.		2,187 ft.											
412 a	Stokers Shifting Room	1915	Walls Studded and weathered boarding Roof - Boarded + Felt. Floor concrete.		3179 ft.	63			4 3/4				GE 406 NT			
419 a	Pump House	1918	Walls Concrete Roof Steel rafters covered corrugated iron. Floor Concrete.		7,260 ft.											
421 a	Vat House	1916	Walls Studded and weather boarded Boarded Roof covered with slates. Floor 2x planking		1248 ft. Building 40,990 ft.								G 412 NT	No foundations measured.		
421 b	Press House	1916	Walls 9" brick - Roof Timber boarded + Felt Floor Asphalt on concrete		2,678 ft.	90			8				G 416 ✓			
422 a	Vat House conversion of N.C. Store	1916	Walls brick - Roof Steel principals, boarded covered with slates. Floor Concrete.		2400 ft. Building 113,740 ft.								G 423 NT			

Map No	Description	When Built	Construction	Dimensions	Cubic Contents			Cost of Building where known			Price per Cubic Foot			Depreciation	Valuation	Remarks	No
					L	s	d	L	s	d	L	s	d				
422 b	Pulping and Moulding Room.	1916	Brick walls & Piers Steel principals, boarded and Roof Asphalts Floor.		130	87	5	L	s	d	L	s	d				
423 a	Cotton Waste Store No. 1.	1913	Studded weather boarded walls. Roof. Timber & boarded covered Ruberoid. Concrete Floor Building. A lean to.		12	40	0										
424 a	Cotton Waste Store No. 3.	1913	Adjoining Egg house. Studded weather boarded walls on Brick dwarf wall 18" above Floor level. Timber & Ruberoid covered Roof. Concrete floor partly flagged.		28	00	6										
430 a	Electric Tractor Charging House.	1917	Weather boarded walls Boarded & Felt Roof Concrete Floor - Lean to off No. 430.		9	78											
434 a	Motor House	1918	Brick walls. Steel Roof Principals, covered Corrugated iron. Floor tarred paved.		9	03											
434 b	House for Nire Cake Crusher, G. C.				12	37	5										
435 a	Drum Shed	1915	Studded and boarded walls - Roof boarded Floor Ashes. Building delapidated.		3	75	4										
436 a	Nitric Acid Factory.	1915	Steel framed Building sides covered corrugated sheets. Steel principals covered boards and felt. Cement floor		159	14	6										
437 a	Absorption Acid Towers.	1918 <i>not finished yet</i>	Adjoining the above 6 brick columns 3'0" x 1'6" on Concrete base Steel joist & Stone slab deck.														

G. 418.  
No foundations measured.

G. 438.

G. 444.

Demolished

Map No.	Description	When Built	Construction	Dimensions	Cubic Contents	Cost of Building where known			Price per Cubic Foot			Depreciation	Valuation	Remarks	No
						£	s	d	£	s	d				
437 b.	Absorption Acid Towers	Not finished	10 Brick piers 2 1/2 feet sq. 9 feet high. no superstructure.												
438 a.	Bicycle Shed.	1915	Open sides and ends covered corrugated iron carried on wooden posts Asphalt floor.		4606'										
438 b.	Ticket Station	1916	Corrugated Iron Sides. open ends. Corrugated round iron Roofs. Asphalt on concrete floor		3646'	23	-	-	1	3			Demolished 1923/24		
439 b.	Timekeepers Office	1916	Studded and weather boarded walls lined with uratite. boarded and felt Roof - wooden floor.		650'	41	-	-	1	3			Demolished 1923 24		
439 c.	Shelter	1917	Open front. Back Ends weather boarded on cement foundations Boarded & felt Roof. Cement floor.		1440 no foundations taken	40	-	-	7	15			Demolished 1923/24 Foundations not measured.		
440	Petrol. Store	1914	9 brick walls - Boarded and felt Roof - wooden Floor		588'										
440 a.	Pay Office	1915	Brick walls. Concrete foundations on piles Timber Roof, boarded and slated - Ceiling matchlined - Wood boarded Floor on splines in concrete.		2994'	111	-	-	9	3			Foundations and piles not measured.		
440 b.	Cotton Waste Store No. 4	1915	Wood framed walls cov. corrugated sheets - Roof Belfast Trusses, boarded covered Felt. Floor 4" P. Cement on Ashes.		83.628'	558	-	-	1	6					
440 c.	Nitrate of Soda Store	1918	Walls Steel Stanchions and reinforced concrete. to 10' 5" above Ground Floor above filled in with 2" concrete slabs - Steel Trusses. Tiled Roof Concrete floor.		112357	355	-	-	7	2					






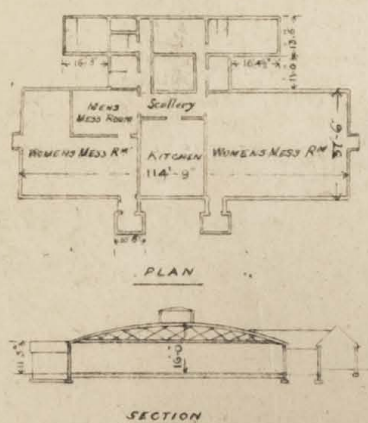
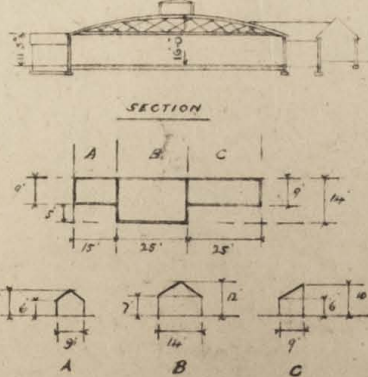

G. 453 ✓

G. 452 NT

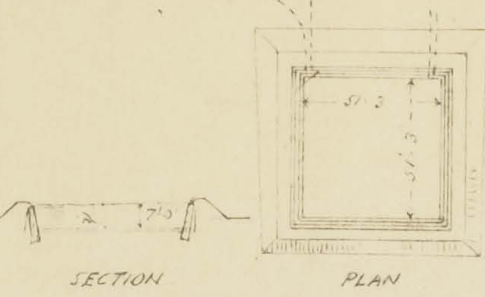






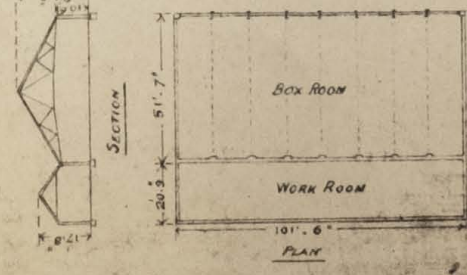
G. 449 ✓  
Foundations and piles not measured.

N. 521. NT



Map No	Description	Where Built	Construction	Dimensions	Cubic Contents	Cost of Building where known.			Price per Cubic Foot			Depreciation	Valuation	Remarks	No
						£	s	d	£	s	d				
453 a	Foreman's Dining Room.	1917	9" Brick walls. Asphalted Flat Roof. Concrete floor.		1728'	160	-	-	1	10			M. 334 ✓		
455 a 455 b.	Drying Room Do. Cloaks.	1916	Two Buildings with opening in partition wall 9" brick walls. Slated Roof. Concrete floor. built as annex to 455.		4992'	342	-	-	1	4 1/2			N. 505 ✓		
455 c.	Womens F.C. (10)	1916	Weather boarded walls. Concrete Floor. Collar Roof. boarded + felt.		1912'	63	-	-		7-9			NB. 511 ✓		
455 d.	Womens Shifting Room	1917 1918 1915	Brick walls. Concrete Floor Timber Roof, boarded and felt Roof. Weather boarded walls Collar Roof with steel tie Concrete Floor		13,125'	542	-	-		00			N. 506 ✓		
455 e	Womens F.C.	1917 1918	Brick walls. Concrete Floor. Corrugated Iron Roof.		3857'	206	-	-	1	0-85			N. 508 ✓		
455 f.	Womens + Mens Dining Room.	1917 1918	Brick walls. Concrete foundations Corred Steel Roof. Asbestos sheeting. Cement floor.		81,041'	3603	-	-		11.			N. 509 ✓		
455 g.	B.W.D. Workshop	1917	A. Rough Shed. Built of old materials. Timber + Felt Roof. Earth floor B. Boarded walls. Tiled Roof Timber floor. C. Lattice timber walls. Felt Roof. Ash floor.		A 9445' B 3325' C 1800'										
455 h	B.W.D. Offices.	1917	Weather boarded walls boarded and felt Roof boarded floor.		380'	15	-	-					NB. 514 ✓		









Map No	Description	When Built	Construction	Dimensions	Cubic Contents	Cost of Building where known			Price per Cubic Foot			Depreciation	Valuation	Remarks	No
						£	s.	d.	£	s.	d.				
460 a	Dry G.C. Yarn Store	1917	Timber framed walls covered rubberoid lined asbestos sheets calico over joists & painted Boarded & felt Roof Lead Floor - Porch Shelter & Tram track		6662	406			1	2 1/2			M. 341 ✓		
464 a	Reservoir	1912	All Concrete Construction. Reservoir 4 feet deep Bottom 6" Portland cement graded 3" to outfall walls stepped from 8" thick on top to 18" thick at bottom.		/										
464 b	Pump House Quinton Hill	1915	Concrete foundation and floor. Brick walls & piers. Wood roof, boarded & slated.											M. 330. ✓	
471 a	Dry Gun Cotton Packing House.	1915	Timber framed & boarded walls Boarded & felt Roof Timber floors & covered lead. On brick foundations 15" above the ground level Lined painted calico.		3785	163.				1034			M. 347. ✓		
472 a	Gun Cotton Yarn Drying Stoves.	1916	Ends & back weather boards Roof, boards and felt. Lead Floor on concrete		1545	141.				1	10				
472 b	Ditto		Timber framed & boarded walls & covered with felt Asbestos Corrugated Sheet		1545	261.				3	4 1/2				
472 c	Ditto		Roof. Motor Houses weather boarded walls Boarded & felted Roofs	Ditto	1545	266	16			3	5 1/2				
472 d	Ditto		Concrete bed for Motors.	Ditto	1545	266	16			3	5 1/2				
472 e	Ditto		Ditto	Ditto	1545	266	16			3	5 1/2				
472 f	Ditto		Ditto	Ditto	1545	266	16			3	5 1/2				
472 g	Ditto		Ditto	Ditto	1545	266	16			3	5 1/2				

Map No	Description	When Built	Construction	Dimensions	Cubic Contents	Cost of Building where known			Price per Cubic Foot			Depreciation	Valuation	Remarks	No
						L	s	d	L	s	d				
1478 a	Reservoir	1915	Reservoir for Gun Cotton Factory Quinton Hill 100 000 gallons capacity		22684	1981	-	-	1	9					
1498 a	Dining Room	1917	Light steel framing and corrugated iron walls and curved corrugated iron roof. Concrete floor.		2072										
510 a	Tractor Charging House	1917													
517 a	Press House No 9.	1915	9" Brick walls & piers. Val-de-Travers Asphalt on Concrete. Quaker Post Roof. Boarded + Felt Roof.		62495	1105	-	-	4	1/2					
517 b.	Latrines	1917	9" Brick Walls. Val-de-Travers Floor on Concrete. Boarded and Felt Roof.		1854										
527 a	Hose House	1917	Timber framed & weather boarded walls on 1/2 brick foundations. Roof boarded + slated. Floor Concrete.		1403										
527 b.	Circular Filter & Sewage Disposul Scheme.	1917	In Concrete. Brick walls Filled with clinkers. Including drainage & conversion of certain E.C into W.C.												
529 a	E.C.S. (4) & TWO URINALS.	1917	Brick Walls. Concrete floor Collar Roof. boarded + Felt		1499	52	-	-	8	1/2			P. 707. ✓		
529 b	Box House.	1915			125316	1950			3	3/4			P. 708. ✓		





Map No.	Description	When Built	Construction	Dimensions	Cubic Contents	Cost of Building where known			Depreciation	Valuation	Remarks	No.
						£	s	d.				
597	Blending House No 5	1916 1917	14 Brick walls. Roof Purlins & boarded and covered felt. Floor Concrete. Steel joists and expanded metal.		54,812	1715					R. 662. ✓	
598	E.C.	Do.	9 Brick Walls. Slated Roof. Concrete floor in 6 Compartments. Urinal & Sand Box.		1650						R. 674 NT	
599	Hose House.	Do.	Timber framed & weather boarded walls on 1/2 brick foundation walls. 12 high Roof boarded and slated Floor Concrete.		1403						R.F. 675 NT	
606	Police Hut.	Do.	Weather boarded walls Concrete & Cement floor boarded & Felt Roof.		3716							
606 a	Cycle Shed.	Do.	Ditto. Ditto.		2100	61			7			
607	Women's Shifting Room and Dining Room.	Do.	Wood framed & weather boarded walls. Part Belfast Truss Roof. Part lean-to. Part Pent Roof. Roof boarded and felted. Kitchen & Offices & Lavatory Cement floor. Remainder wood boards on Joists.		208608	328			6		P. 702. ✓	

Map No	Description	When Built	Construction	Dimensions	Cubic Contents	Cost of Building where known			Price per Cubic Foot			Depreciation	Valuation	Remarks	No
						£	s	d	£	s	d				
607a	Wheel Stretchers House	1918	Wood framed walls & Roof all covered with felt Earth Floor		170										
608	Reel Stove N° 3	1915	14" Brick Walls & 9" division walls. Roof purlins and boarded & covered Ruberoid Floor concrete Steel joints and expanded metal.		14,350	1503			7 3/4					P. 703 ✓	
609	Reeling House N° 2	1915	Brick walls Steel principals Boarded Roof and felt. Concrete floor covered kut de travers Asphalt.		75,068	1910			6-1					P. 704 ✓	
	Do. Verandah	1918	Addition of Verandah to whole length of Building 6 feet wide		7830	128			3-9						
609 <sup>a</sup>	Womens E.Cs (2)	1918	4 1/2" Brick walls Floor Asphalt on Concrete. Boarded & Felt Roof	See Drawing above.	912										
610	Reeling House N° 1	1917	Ditto as above.		94,070	3371			8-1					P. 705 ✓	
	Do. Verandah	1918	Ditto as above.												
611	Womens E.Cs (2)	1918	Ditto as above.	For Sections see above.	912										
612	Corāite Testing House	1915	9" Brick Walls. Iron Roof Trusses. Boarded & Felt Roof Asphalt Floor on Concrete.		7072	236			8					P. 706 ✓	
613	Blending House N° 6	1916	9" Brick walls. Asphalt Floor. Collar Roof boarded & felted. Undermen with boards. Shelter corrugated sides. Felt Roof.		12,312	393			7-6					P. 715 ✓	

